

QUARTERLY PROGRESS REPORT
GLOBAL PARTNERSHIP FOR EDUCATION-BALUCHISTAN EDUCATION PROJECT
SECONDARY EDUCATION DEPARTMENT
GOVERNMENT OF BALUCHISTAN



For the Quarter

Jan – Mar 2018

Project ID- P144454

Prepared by Manager M&E GPE/BEP

Executive Summary: Project Management Unit (PMU), Global Partnership for Education-Balochistan Education Project (GPE-BEP) is implementing a three year project under the supervision of World Bank. The PMU has identified and notified all 725 locations for new primary schools and all 95 primary schools to middle and 25 middle schools to high level for up-gradation with set notified criteria. 1082 teachers have been recruited and deployed for 654 newly established and upgradation schools. Recruitment of all the target teachers under the project is expected to be completed by coming quarter.

Per MIS Dashboard, 1035 total teachers have been trained so far. However, the informal source reports this number as of 1281. PMU is committed to complete the training of all the target 1988 teachers by the end of upcoming second quarter .i.e. Apr-June, 2018.

In the reporting period, K-5 students' total enrollment has been reported as 47597 against 536 new established primary schools, and 118 (93 Middle and 25 High) under establishment up-gradation schools. This enrolment achieves 113% of project total enrolment target of K-5 enrollment where 189 more new schools enrollment is yet to be reported. It is encouraging that PMU expects 10017 more enrolment from the remaining 189 schools at average of 53 enrolment per currently established each school average. This expected enrolment will achieve project enrolment target at ratio of 136% which is highly commendable.

The retention of the students in the project schools have been calculated in the reporting quarter. The students retention is calculated as 81% against the project target of 75% for the project year two. The retention is calculated of 303 schools which have completed their one year study session and started the second year. The target is achieved at ration of 108% which is commendable.

Furthermore, 823 total schools have been advertised for construction works. Contracts have been awarded to start works in 802 schools. Whereas, works have been started in 789 schools.

ECE TLM material has been procured for 365 schools which will be distributed in all 845 schools and will not be procured any further, a taaleemi basta and multi-grade bags have been procured for all the 845 schools instead. In the reporting period, 548 schools have been provided with the TLM kits.

463 schools have been provided with the furniture including blackboard. ECE Program has been established in 654 schools including 536 newly established schools and 118 upgraded schools.

Contents

| | |
|--|----|
| Results based progress | 4 |
| 1. Project Development Objective | 4 |
| 1.1 Girls enrolled in grades K-5 of project supported government schools | 4 |
| 1.2 Boys enrolled in grades K-5 of project supported government schools..... | 5 |
| 1.3 Girls enrolled in grades 6-10 of project supported government schools..... | 5 |
| 2.0. Intermediate Results..... | 7 |
| 2.1. Number of new primary schools established through community support | 7 |
| 2.2. Number of schools upgraded from primary to middle level | 7 |
| 2.3. Number of schools upgraded from middle to high/higher secondary level..... | 8 |
| 2.5. Number of schools to which TLM kits provided..... | 8 |
| 2.6. Number of government schools in which ECE program established | 9 |
| 2.7. Number of PTSMC members trained in targeted project schools | 9 |
| 2.8. Number of teaching staff trained in the project specific schools | 9 |
| 3.0. Detail table of the set target achievement against the result framework | 10 |
| 4.0. Grievance Redressal Mechanism (GRM):..... | 11 |

Results based progress

1. Project Development Objectives

1.1 Girls enrolled in grades K-5 of project supported government schools



- **Progress:** The enrollment of 33850 in the bar chart is the result of the restless effort of all the PMU program sections. The enrolment/schools increased from 27802/507 of the previous quarter to 33850/654 in the reporting period at ratio from 104% to 126% of the total project enrolment target which is highly commendable. The 654 schools given in the bar include the enrolment of 536 newly established and 118 up-gradation schools for the reporting period. The K-5 girls enrolment has been achieved over 100% where 189 schools enrollment are yet to be included.

- **Enrollment Projection:** The remaining 189 schools at this average of 30 per school (when established) will add 5670 more enrolment which will sum the total enrolment as 39520. And this clearly projects that the achievement against this target indicator will be 147% which surpluses 47% of the girls K-5 enrolment to be highly satisfactory.

- **Lesson(s) learned:** While selecting the schools, maximum enrollment-potential locations should be selected.


- **Recommendation(s):** The Education Section

should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools. The TLMs and other materials and the schools buildings should be completed ASAP to avoid the dropout.

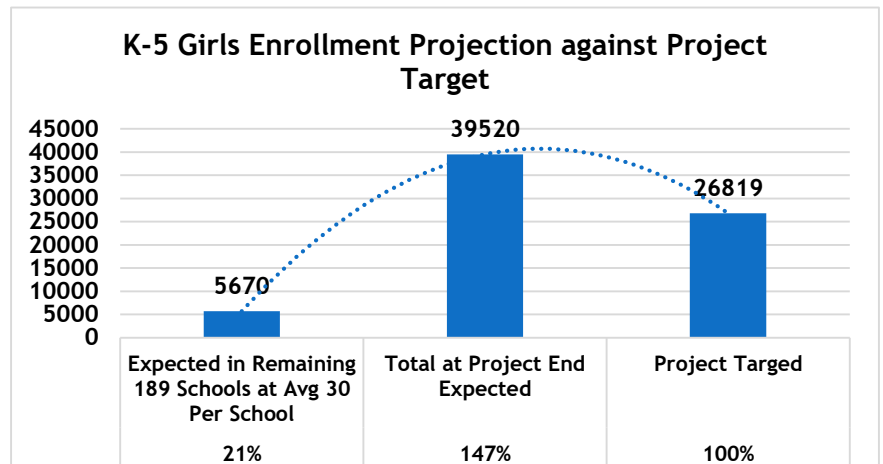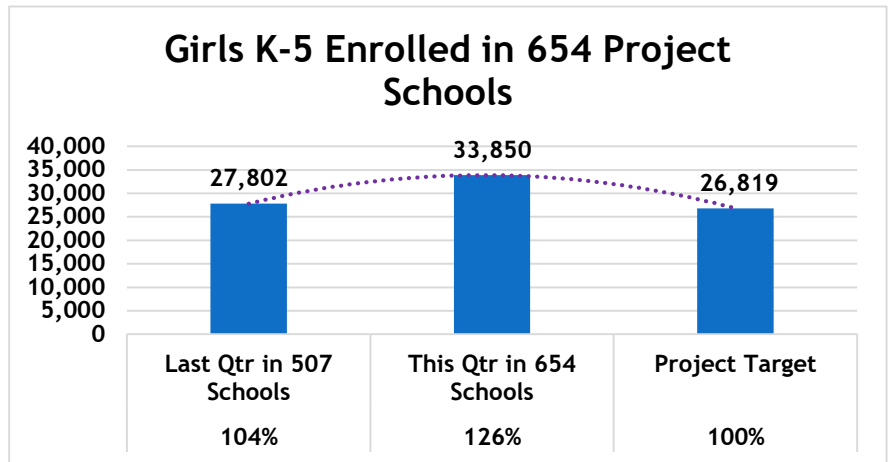


1.2 Boys enrolled in grades K-5 of project supported government schools

- **Progress:** The enrollment of 13747 in the bar chart is the result of the restless effort of all the PMU program sections. The enrolment/schools increased from 9738/507 of the previous quarter to 13747/654 in the reporting period at ratio from 63% to 89% of the total project enrolment target. The 654 schools given in the bar include the enrolment of 536 newly established and 118 up-gradation schools for the reporting period.

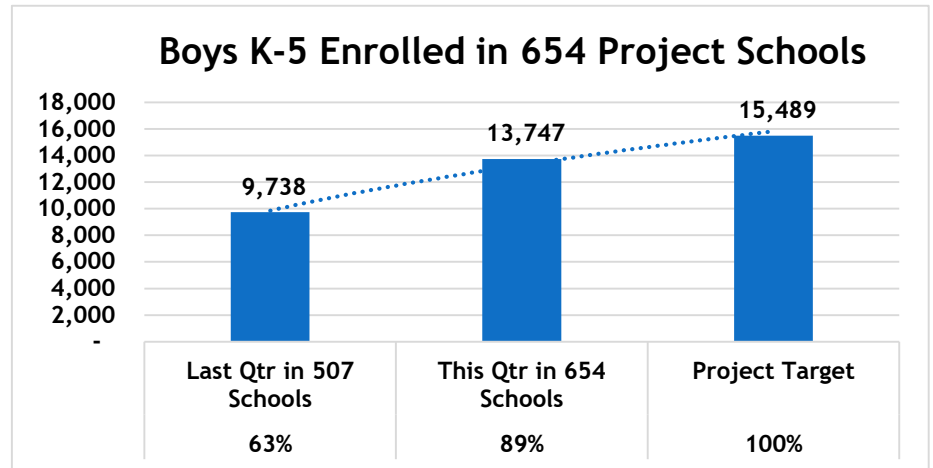

- **Enrollment Projection:** The K-5 boys enrolment achieved so far projects that the remaining 189 schools at this average of 23 per school (when established) will add 4347 more enrolment which will sum the total enrolment as 18094 by the end of the project. And this clearly projects that the achievement against this target indicator will be 117% which surpluses 17% of the boys K-5 enrolment to be highly satisfactory.

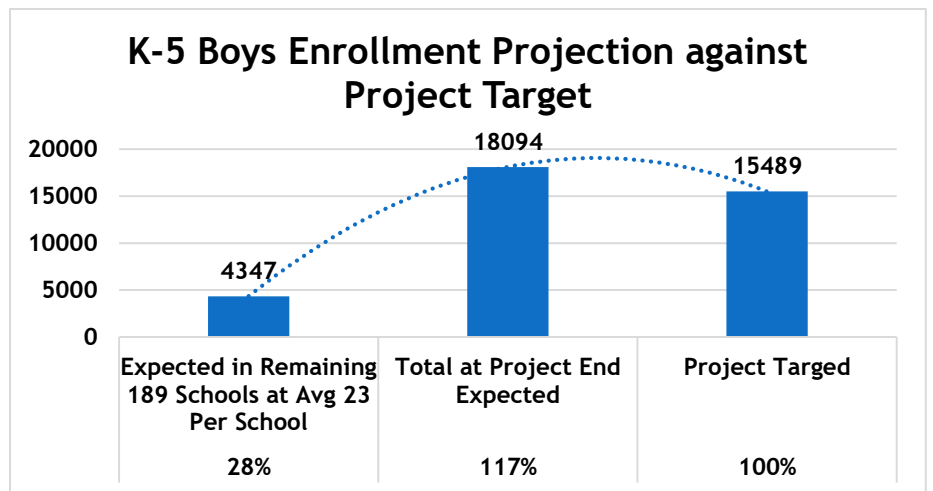


- **Lesson(s) learned:** While selecting the schools, maximum enrollment-potential locations should be selected.

- **Recommendation(s):** The Education Officers should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools. The TLMs and other materials and the schools buildings should be completed ASAP to avoid the dropout.

1.3. Girls enrolled in grades 6-10 of project supported government schools


- **Progress:** The enrollment of 6-10 girls in the reporting quarter is 2945 in 118 schools which is 160% of the set target. This project indicator has been achieved over 100% which is highly satisfactory. The enrollment of girls 6-10 is achieved from project supported upgradation schools. However, the construction works completion, provision of material and teachers arranged for upgraded schools is under process. The upgraded schools have entirely been selected on available higher enrolment and higher potential enrolment for the upgraded levels.

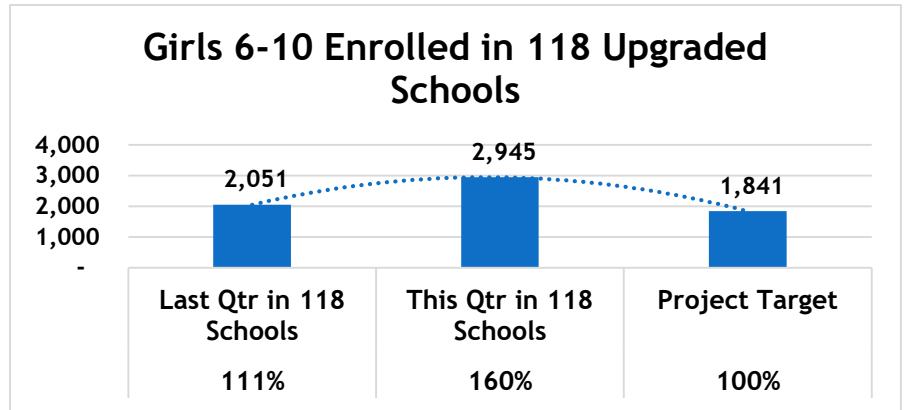

- **Lesson(s) learned:** The schools with high enrolment and feeder schools should be selected for up-gradation.
- **Recommendation(s):** The Education Officers should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools. The TLMs and other materials and the schools buildings should be completed ASAP to avoid the dropout.

1.4. Students retention in project schools

-Progress: The students retention in 303 schools has been calculated as 81% against the 75% target for the year two which determines the response value of the community towards the design and operations of the schools and hard work of the field staff over the mobilization of community to retain the students at the schools. It is very encouraging to see that the target is achieved at the rate of 108%. The target has been calculated for project year two though these 303 schools have completed their year one of the study session. The retention has been calculated with the formula as follows:

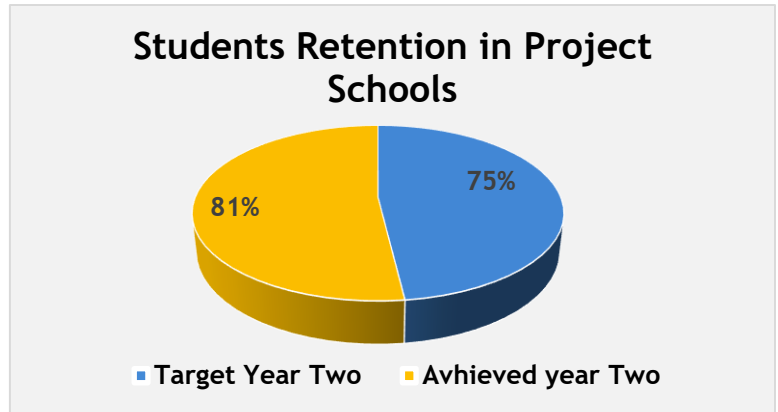

$$\frac{\text{Y2 total enrollment} - \text{Y2 total new enrollment}}{\text{Y1 total enrollment}} \times 100 = \text{Retention}$$

- **Lesson(s) learned:** Regular monitoring and follow up of the students attendance at the schools resulted this encouraging achievement.


2.0. Intermediate Results

2.1. Number of new primary schools established through community support

- **Progress:** The chart shows that 536 of 725 schools have been established. The chart shows that the schools establishment ratio has comparatively been well improved from last quarter as 54% and this reporting period as 74%. 1088 teachers have been hired by the reporting period for 536 primary schools. It is expected that all the due number of the teachers will be completed by the coming quarter.


- **Lessons learned:** The PMU should ensure that all the concerned UCs villages have received the information in regard to applying for the concerned schools. Few of the concerned UCs schools did not apply for the NTS tests.

- **Recommendation(s):** Through all the available means, PMU must ensure that the concerned villages receive the information in regard to schools for applying NTS tests.

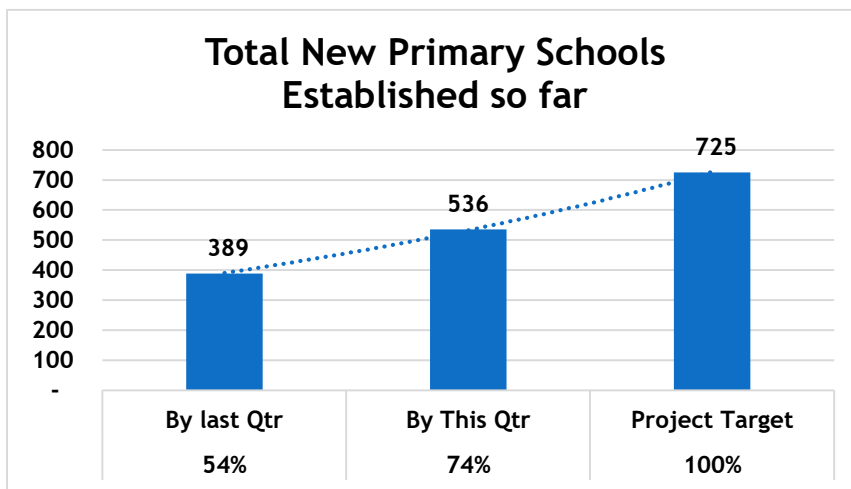


2.2. Number of schools upgraded from primary to middle level

Activity Updates: There is target of 95 middle schools upgradation from the Primary level in the project. All the 95 schools have been identified and notified. PMU has started working on upgradation activities in 99% of the upgraded schools. It is reported that 60 of 94 middle schools have started studied in class 6 contributing into total middle level enrollment of 2595.

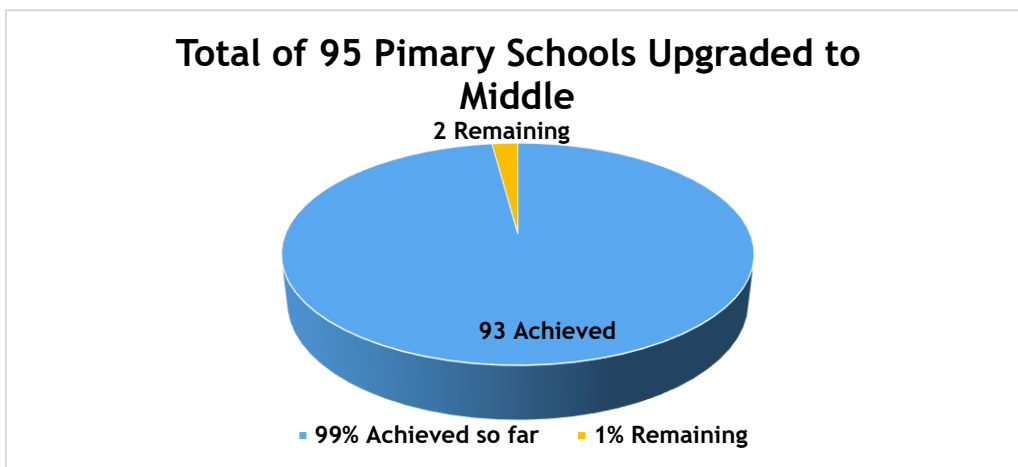


2.3. Number of schools upgraded from middle to high/higher secondary level

Activity Updates: There is target of 25 high schools upgradation from the Middle level in the project. All 25 schools have been identified and notified. PMU has started working on upgradation activities in 100% of the upgraded schools. It is reported that 13 of 25 High schools have started studied in class 9 contributing into total high level enrollment of 338.

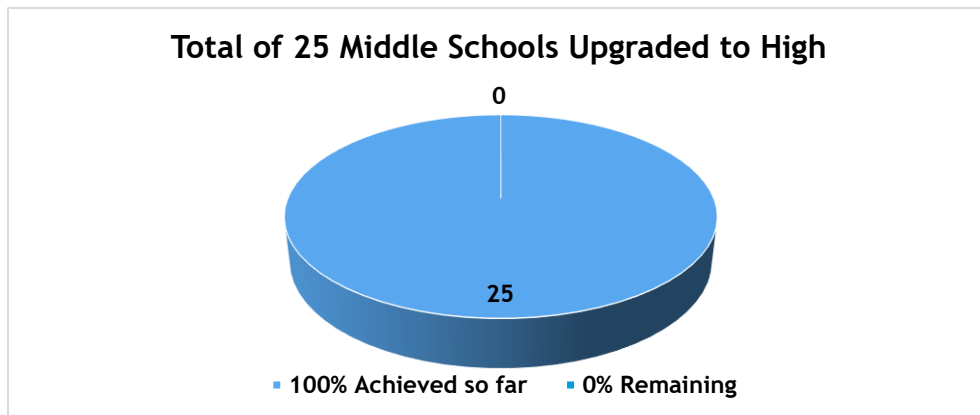

2.4. Number of government schools to which furniture (incl blackboard) is provided


Activity Updates: The procurement of all the target schools have been made. PMU has provided 463 of 845 schools with the furniture including blackboard in the reporting period. However, PMU has planned to provide all schools with furniture including blackboard in the coming quarter.

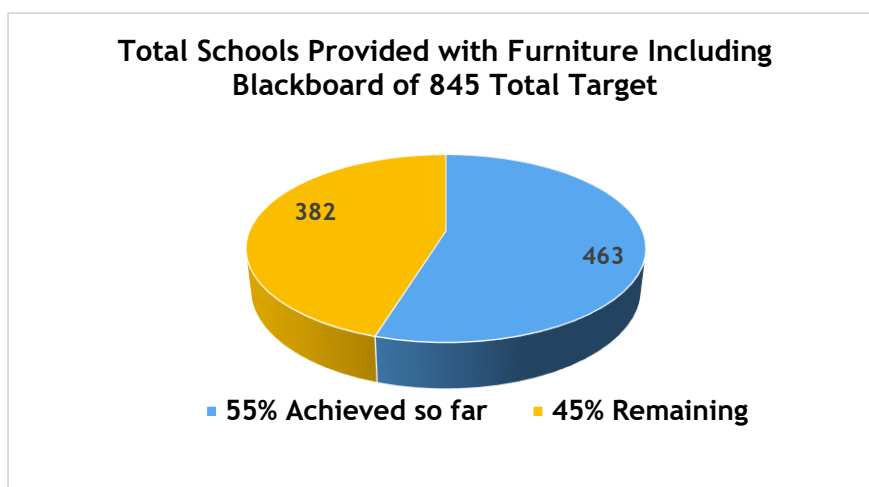

2.5. Number of schools to which TLM kits provided

Activity Updates: All ECE TLM 365 Kits have been procured which will be distributed among all 845 schools and will not be procured any further, a taaleemi basta and multi-grade bags have been procured for all the 845 schools instead.


The chart reports that PMU has provided 548 of 845 schools TLM kits so far. However, it plans to provide all schools with the TLM kits in the coming quarter.

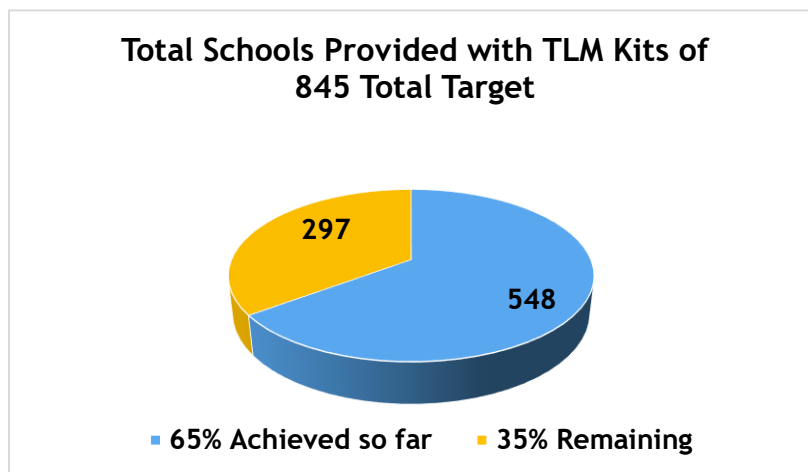

2.6. Number of government schools in which ECE program established

Activity Updates: 654 of 845 schools are established with the ECE program under the project. The project target number is expected to be achieved in the coming quarter. Due to split items procurement and wide spread field, the ECE materials takes time while supplying. However, the PMU has improved the supply and distribution plan and will expedite the supply and distribution in a much improved manner with complete supply in the coming quarter.


Total of 845 Schools with ECE Program Established

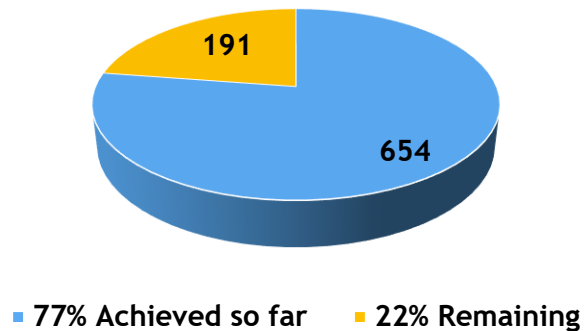

2.7. Number of PTSMC members trained in targeted project schools

Activity Updates: The number of the PTSMC members has been improved as compared to previous quarter. 1313/29% of 4465/100% PTSMC members have been trained in the reporting period. The trainings are going on. PMU expects to complete the training of all the PTSMC members by the end of the project this year.

Total PTSMC Members Trained against Target Total 4465

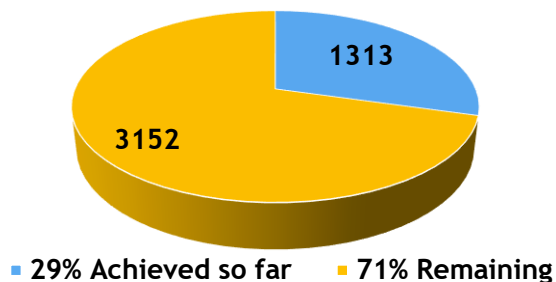


2.8. Number of teaching staff trained in the project specific schools

Activity Updates: The pie chart shows that 1035 of total target teachers have been reported trained so far. This proportionate to have achieved 52% of the total project target as per dashboard so far. However, the informal source reports that there are still 263 teachers trained but yet not updated over the MIS dashboard. Including this un-updated number, it will sum the teachers trained number as 1281 which is 64% of the total target teachers.

PMU has planned the trainings for the remaining teachers in coming quarter. The progress improves each quarter. It is shared that all 1988 teachers will be trained by the close of the coming quarter .i.e. Apr-June, 2018.

Total Teachers Trained of Target 1988



3.0. Detail table of the set target achievement against the result framework

| Project Development Objectives | Target | Status | Remarks |
|---|--------|--------|---|
| Girls enrolled in grades K-5 of project supported government schools | 26819 | 33850 | 126% Target achieved |
| Boys enrolled in grades K-5 of project supported government schools | 15489 | 13747 | 89% Target Achieved |
| Student retention in project schools | 75% | 81% | 108% Target Achieved (the target has been calculated as of year two though these 303 schools have completed their first study session) |
| Girls enrolled in grades 6-10 of project supported government schools | 1841 | 2945 | 160% Target Achieved |
| Intermediate Results | | | |
| Number of new primary schools established through community support | 725 | 536 | 74% Target Achieved |
| Number of schools upgraded from primary to middle level | 95 | 93 | 99% (However, it is reported that 60 schools have started class 6 th study session) |
| Number of schools upgraded from middle to high/higher secondary level | 25 | 25 | 100% (However, it is reported that 13 schools have started class 9 th study session) |
| Number of government schools to which furniture (incl blackboard) is provided | 845 | 463 | 55% Target Achieved |
| Number of schools to which TLM kits provided | 845 | 548 | 65% Target Achieved |
| Number of government schools in which ECE program established | 845 | 654 | 78% Target Achieved |
| Number of PTSMC members trained in targeted project schools | 4465 | 1313 | 29% Target Achieved |
| Number of teaching staff trained in the project specific schools | 1988 | 1035 | 52% Target Achieved |
| Project reports generated on selected indicators | | | |

4.0. Grievance Redressal Mechanism (GRM):

Table B (detailed sheet attached as Annex-A)

| Summary of BEP-GRM Cases | | | | | | |
|---------------------------------|-------------------------------|--------------------------|----------------------|-------------------------------|--------------------------|----------------------|
| Description | Cases by Jul-Sep, 2017 | | | Cases by Jan-Mar, 2018 | | |
| | Total Filed | Total Disposed of | Total Pending | Total Filed | Total Disposed of | Total Pending |
| *CRC/General Complaints | 50 | 47 | 3 | 50 | 50 | 0 |
| Court Cases | 9 | 2 | 7 | 30 | 9 | 21 |
| Procurement Cases | 5 | 5 | 0 | 5 | 5 | 0 |
| Total | 64 | 54 | 10 | 85 | 64 | 21 |

**CRC/General Complaints include all the complaints submitted to confirm schools selection, NTS tests, and Teachers selection. Since CRC-Complaint Redress Cell is chaired by concerned division honorable Commissioner at Division level, PMU does not have any mandate to redress the cases falling under the CRC level specifically in regard to teachers selection. However, PMU GRM-PAC receives the complaints and guides the complainants to move to the CRC to file their complaint.*

5.0. ESMP Quarterly Progress Report Jan-Mar, 2018

| Construction stage | | | | | | | | | |
|--|-------------|---------------|------------------------------------|-------------------------------------|------------------------------------|-------------------------------------|--|--------------|---------------------------------|
| Balochistan Education Project Quarterly ESMP Implementation and Checklist Status | | | | | | | | | |
| S. No | District | Total Schools | Data Received during First quarter | Data Received during second quarter | Data Received during third quarter | Data Received during fourth quarter | ESMP Checklist Filled Construction stage | Key Findings | Remedial Actions Taken (if any) |
| 1 | Quetta | 28 | 2 | | | | No issue regarding construction reported | | |
| 2 | K abdullah | 39 | 9 | | | | No issue regarding construction reported | | |
| 3 | Mastung | 19 | 0 | | | | No issue regarding construction reported | | |
| 4 | Pishin | 29 | 3 | | | | No issue regarding construction reported | | |
| 5 | Awaran | 21 | 2 | | | | No issue regarding construction reported | | |
| 6 | Khuzdar | 35 | 11 | | | | No issue regarding construction reported | | |
| 7 | Kalat | 25 | 3 | | | | No issue regarding construction reported | | |
| 8 | Lasbella | 54 | 14 | | | | No issue regarding construction reported | | |
| 9 | Hernai | 20 | 0 | | | | No issue regarding construction reported | | |
| 10 | K saifullah | 35 | 7 | | | | No issue regarding construction reported | | |
| 11 | Sherani | 20 | 2 | | | | No issue regarding construction reported | | |
| 12 | Zhob | 40 | 6 | | | | No issue regarding construction reported | | |
| 13 | Ziarat | 25 | 1 | | | | No issue regarding construction reported | | |

| | | | | | | | | | |
|----|-------------|----|----|--|--|--|--|--|--|
| 14 | Barkhan | 31 | 2 | | | | No issue regarding construction reported | | |
| 15 | Kohlu | 17 | 2 | | | | No issue regarding construction reported | | |
| 16 | Loralai | 30 | 0 | | | | No issue regarding construction reported | | |
| 17 | Musakhail | 27 | 0 | | | | No issue regarding construction reported | | |
| 18 | Dera Bughti | 32 | 1 | | | | No issue regarding construction reported | | |
| 19 | Jaffarabad | 28 | 4 | | | | No issue regarding construction reported | | |
| 20 | Jhal Magsi | 20 | 2 | | | | No issue regarding construction reported | | |
| 21 | Kachi | 20 | 2 | | | | No issue regarding construction reported | | |
| 22 | Naseerabad | 46 | 25 | | | | No issue regarding construction reported | | |
| 23 | Sohbatpur | 28 | 5 | | | | No issue regarding construction reported | | |
| 24 | Sibi | 19 | 3 | | | | No issue regarding construction reported | | |
| 25 | Chaghi | 30 | 11 | | | | No issue regarding construction reported | | |
| 26 | Kharan | 29 | 6 | | | | No issue regarding construction reported | | |
| 27 | Noshki | 25 | 14 | | | | No issue regarding construction reported | | |
| 28 | Washak | 19 | 3 | | | | No issue regarding construction reported | | |
| 29 | Gwadar | 25 | 0 | | | | No issue regarding construction reported | | |
| 30 | Kech | 26 | 0 | | | | No issue regarding construction reported | | |
| 31 | Punjgoor | 22 | 2 | | | | No issue regarding construction reported | | |

6.0. Total 142 construction stage checklists have been received by the reporting quarter of 2018.

Status of completion of ESMP remedial actions

| S.No | District | Region | ESMP Checklist Filled Siting stage | Key findings | Remedial Action taken (If any) | Current status | Estimated Cost |
|------|----------|--------|------------------------------------|--|--|---|----------------|
| 1 | Quetta | 1 | GGPS Killi Mehrab khan Kuchlak | Transmission lines are passing near the boundary wall of a school. | Keeping in view the location of transmission lines the building is planned on the opposite site of a school building which is safe for the construction. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security. | Not yet completed Construction work has stopped. | Rs. 200000/- |
| 2 | Quetta | 1 | GPS Shaheed Aymal kasi | Adjacent to solid waste dumpster | Members of PTSMCs have been contacted to remove waste from the school site. | (Contractor has been contacted and at the time of construction the waste will be removed) | - |
| 3 | Quetta | 1 | Shin Kach Hanna | Near Flood pathway | Trench will be made to divert flood water | | Rs.20000 |
| 4 | Quetta | 1 | GGPS Gulshan Hassan | Transmission line is passing over the school site. | Concerned department has been contacted and it was told that the transmission line is (HT) and it cannot be replaced. | | |
| 5 | Quetta | 1 | Zarat Colony | Transmission lines are passing over the selected site | Relocation of transmission line is underway with the concerned department. In case it doesn't get final then the transmission lines will be covered with the rubber | | Rs. 200000/- |

| | | | | | | | |
|----|------------|---|---|---|---|---|--------------|
| | | | | | pipe to ensure children safety. | | |
| 6 | Pishin | 1 | Shin Kantay zai | Site situated in flood pathway | Retaining wall will and land levelling required. | Underway | Rs.400000/- |
| 7 | K Abdullah | 1 | GPS Killi Agha Jan Alizai | Disputed land | Relocation of school site is under discussion. | Dropped out | - |
| 8 | K Abdullah | 1 | GPS Killi Haji Abdul Manan Toba | School site is located on top of hill | Land levelling is required | Completed | Rs.60000 |
| 9 | K Abdullah | 1 | GPS Killi Mohammad Yousaf Azadzai Dobandi | Disputed land | Relocation of school site is under discussion | New site has been finalized | - |
| 10 | Lasbela | 2 | Madina Colony | Transmission line is passing over the selected site. | Relocation of transmission line. Low Transmission Line (LT) but the wires are very high and casing cannot be put on them. In case transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security. | Pole has not been taken out of school building but for the safety of school children pole has been filled with mud. | Rs. 200000/- |
| 11 | Lasbela | 2 | Jam Yousaf colony | Transmission line is passing over boundary wall of school building. | Relocation of transmission line or put casing on the transmission line. In case transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security. | High Transmission Line (HT) Poles can't be replaced but casing will be put on the wires for the safety of school children | Rs.40000/- |

| | | | | | | | |
|----|----------|---|-------------------------------|---|---|---|--------------|
| 12 | Lasbela | 2 | Pathar Colony | Site is located near flood pathway | Stone pitching wall is proposed to safe building from flood water. | In process | Rs.500000/- |
| 13 | Lasbella | 2 | GGMIDS Kumacha | This school is adjacent to river and fall in a flood pathway. | A retaining wall to control flood water has been incorporated in school plan to provide safe environment for the students. | | Rs.1200000 |
| 14 | Zhob | 2 | GGPS Shahbzai | Transmission lines are passing over the selected site | Relocation of transmission line is underway with the concerned department. In case it doesn't get final then the transmission lines will be covered with the rubber pipe to ensure children safety. | Discussion with concerned department is underway. | Rs. 200000/- |
| 15 | Ziarat | 2 | GPS Azogi parshi | Disputed land | | Issue resolved | - |
| 16 | Ziarat | 2 | GPS Baba kharwari ghohira | Disputed land | | Issue resolved | - |
| 17 | Ziarat | 2 | GPS KharShang | Disputed land | | Issue resolved | - |
| 18 | Ziarat | 2 | GPS Narai Daag Fatah Muhammad | Disputed land | | Issue resolved | - |
| 19 | Ziarat | 2 | GGPS Kan depot. | The school site is close to highway | A traffic sign indicating school is close will be installed on the highway at the visible place. | Not yet completed | Rs.10000/- |
| 20 | Ziarat | 2 | GGMIDS Pitao Zindra | The school site is close to highway | A traffic sign indicating school is close will be installed on the highway at the visible place. | Not yet completed | Rs.10000/- |

| | | | | | | | |
|----|-----------|---|---|---|--|-------------------|--------------|
| 21 | Barkhan | 3 | Rakhni City near Wapda Grid station. | The school site is close to highway | A traffic sign indicating school is close will be installed on the highway at the visible place. | Not yet completed | Rs.10000/- |
| 22 | Barkhan | 3 | PS Basti Tariq Mehmood | Site located in flood pathway | | | |
| 23 | Barkhan | 3 | GGPS Bagra Badiani | Transmission line is passing over the school site. | | | |
| 24 | Kohlu | 3 | GGPS Killi Haji Mohammad | Site located in flood pathway | | | |
| 25 | Kachi | 5 | GGPS Muhallah Muhammad Ali Meerzai Abad | Transmission lines are passing over the selected site | Relocation of transmission line is underway with the concerned department. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security. | Not Yet completed | Rs. 200000/- |
| 26 | Kachi | 5 | GGPS Muhallah Muhammad Ali Meerzai Abad | Transmission lines are passing over the selected site | Relocation of transmission line is underway with the concerned department. In case it doesn't get final then the transmission lines will be covered with the rubber pipe to ensure children safety. | | |
| 27 | Sohbatpur | 5 | GGPS Siandad Kanrani | The school site is close to dumpster | DFP of concerned district has been contacted to relocate the dumpster. | Not Yet completed | - |

| | | | | | | | |
|----|--------|---|------------------------------------|--|---|--|--------------|
| 28 | Sibi | 5 | Elementary College | Transmission line is passing in school building | Relocation of transmission line. In case transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security. | Transmission line can't be relocated but casing will be put on the wires for the safety of school children | Rs.40000/- |
| 29 | Washuk | 6 | GPS Killi Gohari Mir barkat mulazi | Transmission line is passing in school building | Relocation of transmission line. In case transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security. | Concerned department has been contacted for the relocation of transmission line. | |
| 30 | Gwadar | 7 | Senator Ishaq | Transmission line is passing from the school building, | Relocation of transmission line. In case transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security. | Transmission line is not yet relocated | Rs. 200000/- |
| 31 | Gwadar | 7 | GGPS Zahar Bahar | Site adjust to Highway | Traffic sign to be installed | | Rs.10000 |
| 32 | Kech | 7 | GGPS Nokabad Hoshab | Site is close to Highway | | | Rs.10000 |

Annexure-A

| General Complaints | | | | | | | | |
|--------------------|--------------|------------------------------|---|--|-------------------------|--|--|---|
| Sr # | Date | Name of the Complainant | Address With Phone Number | Gist of the Complaint | Time fixed for disposal | Whether Complaint redressed or not (Y/N) | If yes the gist of redressed | If rejected Give Reason |
| 1 | 03-Jan-16 | Jamila Hassan | Nawa Kili Quetta 0304-3324241 | Complaint application was submitted regarding NTS merit list UC Nawa kili | - | Yes | Complainant wanted to exclude ADE marks of qualified candidate. Her request was rejected by District Recruitment Committee as not valid. In recruitment policy issued by Education Department, ADE marks is applicable. | It is against Recruitment Policy notified by Education Department |
| 2 | 02-May-16 | Sain Dad | Sohbatpur Ghot Sain Dad kandani | Submission of letter (Subject: Cancellation of land mutation) for his candidate was not shortlisted in NTS merit list. | 03-05-16 | Yes | The complainant wanted District Recruitment Committee to consider her candidate in lieu of provision of land. However, the Recruitment in the project is made through merit based recruitment policy as notified by Education Department. Therefore, complaint was rejected and recruitment is made on merit based only. | Recruitment of teacher is made on merit basis only, as per notified policy by Education Department. |
| 3 | 2nd May-2016 | Wali Dad | Qaisarabad Sohbatpur 0343-3788221 | Complaint application was submitted regarding unfair recruitment of teacher, for he has devoted land for school and wants his candidate to be short-listed for his UC. | 2nd May-2016 | Yes | The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council. | Recruitment of teacher is made on merit basis only, as per notified policy by Education Department. |
| 4 | 22-Jun-16 | Bilqees D/o Nabi Dad | Lasbela UC Liyari | (JVT complain application was submitted) Complain application was regarding discrimination objection on NTS criteria | 22-06-16 | Yes | Applicant was ineligible because she is not Intermediate pass(which is basic qualifying criteria for teachers) and also she didn't qualify NTS test. | Recruitment of teacher is made on merit basis only, as per notified policy by Education Department. |
| 5 | 22-Jun-16 | Maryam D/o Muhammad Siddique | Lasbela UC Uthal | (JVT complain application was submitted) The community had devoted land for school on one condition iff their candidate be shortlisted. | 22-06-16 | Yes | The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council. | Recruitment of teacher is made on merit basis only, as per notified policy by Education Department. |

| | | | | | | | | |
|----|-----------|---|-----------------------------|--|----------|-----|---|---|
| 6 | 22-Jun-16 | Rehana D/o Yar Muhammad | Lasbela UC Uthal | (JVT complain application was submitted) In application it is stated that the community had devoted land for school on one condition iff their candidate be shortlisted. | 23-06-16 | Yes | The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council. | Recruitment of teacher is made on merit basis only, as per notified policy by Education Department. |
| 7 | 24-Jun-16 | Sumaira D/o Abdul Hakim | Lasbela UC Winder | Complain application was regarding discreamentative objection on NTS criteria | 24-06-16 | Yes | – | Applicant was not eligible because she is not FA and also she didn't qualified NTS test. |
| 8 | 25-Jun-16 | Samiya Khair D/o Khair Muhammad | Rehmdwa Noshki | (JVT complain application was submitted). Objection on merit list finalized by District Recruitment Committee. | 07-07-16 | Yes | District Recruitment Committee considered her request and issue is resolved. | – |
| 9 | 26-Jun-16 | Saima D/o Din Muhammad | Lasbela UC Lakhara | (JVT complain application was submitted) she claims though she has done metriculation but is not shortlisted in NTS merit list. | 26-06-16 | Yes | Required qualification intermediate. She is matriculate thus District Recruitment Committee rejected her complaint. | Applicant was not eligible as per approved criteria |
| 10 | 27-Jun-16 | Saqiba D/o Abdul Razzaq | Loralai UC Zingewal Kotazai | (JVT complain application was submitted). Complain was stated regarding rectification of UC | 24-11-16 | Yes | District Recruitment Committee has verified the documents of candidates and issue was resolved | – |
| 11 | 28-Jun-16 | Raj Bibi D/o Muhammad Ali | Lasbela UC Uthal | (JVT complain application form was submitted) She claimed that her B.Ed and M.A degree was not considered while finalizing NTS merit list. | 05-07-16 | Yes | District Recruitment Committee Lasbela considered her application and it was resolved on merit. She is on 7th number in merit | – |
| 12 | 28-Jun-16 | Mehbooba D/o Paida Khan 0334-2811516 | Kili Saghri Loralai. | Mrs. Mehbooba compliants, that she has secured 50 marks whereas in merit list she has given only 43 marks. | 24-11-16 | Yes | Issue resolved by District Recruitment Committee, on the basis of complaint merit list were checked and made correction in the numbers of the complainant. | – |

| | | | | | | | | |
|----|-----------|-----------------------------------|---------------------|--|----------|-----|---|--|
| 13 | 29-Jun-16 | Sakina Bibi D/o Aziz Khan | Loralai UC Zangewal | Mrs. Sakina bibi complained that she has passed NTS test but her name is missing in merit list. | 24-11-16 | Yes | Issue is resolved, as on the basis of her complaint the merit list was tallied and found that her name was missing due to non-availability of her documents, but on submission/presentation of complete documents her name was included in revised merit list. | - |
| 14 | 30-Jun-16 | Razai Taj D/o Abdul Ghani | Loralai UC Ponga | C.T and B.A marks were not included in NTS merit result. | 24-11-16 | Yes | Case was forwarded to District Recruitment Committee and requested to include her CT and BA Marks, District Recruitment Committee verified her documents and included her marks in the merit list. | - |
| 15 | 04-Jul-16 | Razia D/o Yar Muhammad | Lasbela UC Winder | The candidate has declared the test and is rejected for her qualification is metric and other candidate from other UC is selected. | 15-07-16 | Yes | She is Matriculate only and does not meet eligibility criteria and therefore was not shortlisted and if no candidate is selected on UC level then on tehsil level candidate will be selected. | Required qualification for JVT post is intermediate with 2nd division. |
| 16 | 04-Jul-16 | Gul Bushra Kakar D/o Abdul Ghafor | Loralai UC Ponga | (JVT complain application was submitted) B.A and ADE marks not included | 01-11-16 | Yes | Issue resolved by District Recruitment Committee, the case was forwarded to District Recruitment Committee and requested to include her BA marks, District Recruitment Committee checked her documents and included BA and ADE marks as a result she secured 2nd position and got contract. | - |
| 17 | 07-Jul-16 | Hameeda D/o Muhammad Farooq | Loralai UC Ponga | Complain was stated regarding rectification of UC | 24-11-16 | Yes | Issue resolved by District Recruitment Committee, On the basis of her complaint, Locals of other candidates were checked and found that on candidate were not belonging to here UC and excluded all the candidates from merit list who were not belonging to the same UC. | - |

| | | | | | | | | |
|----|-----------|---------------------------------|-------------------------------------|---|--------------|-----|---|---|
| 18 | 11-Jul-16 | Shahida D/o Jumma Khan | Lasbela UC Wayara | (JVT application was submitted) The community had devoted land for school on one condition iff their candidate be shortlisted and a candidate from other UC is shortlisted. | 21-07-16 | Yes | Firstly she did not pass NTS test secondly if no candidate is selected on UC level then on tehsil level candidate will be selected. | District Recruitment Committee rejected the complaint because it is not in recruitment policy |
| 19 | 29-Jul-16 | Gulshan W/o Noorullah | Lorlai UC Thal | Higher education marks are not included in NTS merit list. | 25-11-16 | Yes | Issue resolved by District Recruitment Committee, the case was forwarded to District Recruitment Committee and requested to include her BA marks, District Recruitment Committee checked her documents and included BA and ADE marks as a result she secured 2nd position and got contract. | - |
| 20 | 01-Oct-16 | Khan Meer | Zhob UC Wala Akram | The UC topper Ms.Farzana Zareef does not belong to UC Wala Akram but to UC Omzha(Rectification of U.C) | 14-10-16 | Yes | Case resolved by District Recruitment Committee on 24-Dec-2016, | - |
| 21 | 01-Nov-16 | Gulshan Bibi D/o Abdul Khalique | Qila Saifullah UC Sadar Muslim bagh | It was stated in complain that her B.Ed marks were not included in merit list. | 01-12-16 | Yes | Issue was addressed to District Recruitment Committee. Marks added as per documents provided | - |
| 22 | 01-Nov-16 | Fatima Bibi D/o Hassan Khan | Qila Saifullah UC Bandad Mir zai | Complain was stated regarding rectification of UC | 01-12-16 | Yes | UC Rectified by District Recruitment Committee as per documents | - |
| 23 | 01-Nov-16 | Zarina Kakar | Qila Saifullah UC Sadar Muslim Bagh | Objection on ADE marks separately. | 01-12-16 | Yes | Issue was addressed by District Recruitment Committee. | - |
| 24 | 03-Nov-16 | Binish Kanwal | Quetta ,Kechi Baig | Complaint for JV teacher's recruitment. She claimed her name is not included in merit list. | 3rd Nov-2016 | Yes | Ms.Binish Kawal is included in merit list on 78th number, her total obtained marks are 57.25, her basic qualification is B.A because her F.A was scored in 3rd div. | - |
| 25 | 03-Nov-16 | Fatima D/o Pehlwan | Qila Saifullah UC Sadar Muslim Bagh | Complain was stated for her B.A marks were not included in NTS merit result. | 01-12-16 | Yes | Issue was addressed to District Recruitment Committee. Marks added as per documents provided | - |

| | | | | | | | | |
|----|--------------|----------------------------------|-------------------------------------|---|---------------|-----|--|--|
| 26 | 04-Nov-16 | Sadiqa D/o Nadir Khan | Qila Saifullah UC Sadar Muslim Bagh | B.Ed and Physical education marks are not included in NTS merit result. | 04-11-16 | Yes | Issue was addressed to District Recruitment Committee. BE.d Marks added as per documents provided, But physical education can't be added because they are not relevant . | - |
| 27 | 04-Nov-16 | Mir Alam Shahwani | Quetta 0333-7812784 | Complaint was recorded regarding NTS result. Ms.Rahila Rahim had her B. Ed degree with her and is not short listed. | 05-11-16 | Yes | DRC considered her request but she is on 85th number in merit | PTC Percentage has been given instead of B.Ed according to policy. And she is on 85th in merit list. |
| 28 | 04-Nov-16 | Khair un Nisa | Qila Saifulla UC Sadar Muslimbagh | Rectification of merit list (The Qualification marks were not included in merit list) | 01-12-16 | Yes | Marks got added in merit, Rectified by District Recruitment Committee | - |
| 29 | 04-Nov-16 | Sardar Bibi & Dowlat Bibi | Qila Saifulla UC Bandad Mirzai | Complain was stated regarding rectification of UC | 01-12-16 | Yes | Candidate added in her UC as per her Local/residential certificate. Rectified by District Recruitment Committee | - |
| 30 | 05-Nov-16 | Gul Sumaira D/o Qalandar Khan | Zhob UC Meena Bazar | Objection on not including B.A marks in NTS merit result. | 24-12-16 | Yes | Issue resolved by District Recruitment Committee . Marks added as per documents provided. | - |
| 31 | 11-Nov-16 | Razia Gul D/o Haji Muhammad Syed | Qila Saifullah UC Sadar Muslim Bagh | Complain was stated regarding rectification of UC | 02-12-16 | Yes | Candidate added in her UC as per her Local/residential certificate. Rectified by District Recruitment Committee | - |
| 32 | 11-Nov-16 | Froza Khanum | UC Narezai | Complain application was regarding NTS merit list | 24-12-16 | Yes | Candidate were informed about final merit as per NTS result and District Recruitment Committee working. issue resolved by District Recruitment Committee | - |
| 33 | 2nd Dec-2016 | Muhammad Rafique | Musa Khail 0335-7418858 | Complaint was submitted on subject of school selection. He claimed that the selected school in his town is located on 50 meters only while the school they applied for is located on 2 km distance and the enrolment of students too is more than the selected school . | 27th Dec-2016 | Yes | On this complaint, PMU has formed a committee of SMIP team and sent to re-visit the selected site (Killi Dargai hassankhail) and committee reported that there is no government school at the distance of 02 Km from the site. A report with GPS coordinates has been verified by SMIP team. | - |

| | | | | | | | | |
|----|---------------|--------------------------------------|-----------------------------|---|------------------|-----|---|-----------|
| 34 | 26th Dec-2016 | Abdul Sattar | Zhob 0313-8820907 | Complaint application was submitted regarding Final Merit list of NTS test for JVT, his candidate Ms. Ameer Bakhta was 3rd in the list though she had her PTC degree with her and the candidate who was at the 2nd number had no PTC degree but that candidate had higher marks in NTS. | 26th Dec-2016 | Yes | His case was dealt by Naseebullah (M&E Manager), Jahanzeb Nasar(Legal Officer) and Kulsoom (Program Associate). The team listened to his complain and was explained the recruitment policy in detail , the complainant was satisfied then. | - |
| 35 | 28th Dec-2016 | Abdul Aziz | Washuk 0336-3959675 | Submission of letter (Subject: Cancellation of land mutation) for his candidate was not shortlisted in NTS merit list. | 2nd Jan-2016 | Yes | The case has been resolved the land mutated | Resolved. |
| 36 | 30th Dec-2016 | Khaliqdad | Muslim Bagh 0335-2700714 | In advertisement the U.C for which candidate Ms.Khair un Nisa was shortlisted was Sultan Zai but actually the school is situated in Sara Gharh U.C, so Mr.Khaliqdad came to discuss the case with concern officer, for officer was not available so Naseebullah (M&E Manager) dealt. | 21st Feb, 2017 | Yes | Babar Jaffar (E.O) dealt the case and complainant was told that letter is sent to DC for verification of UC , as soon as UC is verified he shall be informed by BEP team. After Final merit got signed, DRC received several complaints against merit regarding UCs issue. This issue is highlighted under DRC which is being addressed. The revised final merit will be signed in coming week. | - |
| 37 | 12-Mar-17 | Tayyeba Rassheed 5310342662581 | Kachhi Bolan | The complaint was received via e.mail . There was mentioned that the candidat Ms.Tayyeba Rasheed had applied for the post of JVT for a school in 2013 but she was not selected and there were 3 posts vacant and only one candidate was selected . As two posts are vacant so BEP should assign the vacant post to the above mentioned candidate. | 13th March 2017. | Yes | The complain was discussed with Abdul Qayyum (Program Assistant) called the candidate and talked to her husband and told the complainant that this case belongs to PGEB project which is afterwards handed over to Government, so the Complainent should submit his request to Education Department but he(The candidate's husband) was rudely denying the fact and said that if your project will not facilitate us then i will go to world bank against you people. | Resolved. |

| | | | | | | | | |
|----|-----------------|--|-------------------------|---|------------|-----|---|-----------|
| 38 | 15-Mar-17 | Muhammad Naveed | Barkhan 0333-7736238 | The complain was received via text on our official contact number, there was stated that the applicant Muhammad Naveed has appeared in test for (MonitoringAssociate) in RTSM PMC on 20th Nov-2016 and he also appeared in interview on 13th Dec-2016 but still has no clue about final selection. | 15-Mar-17 | Yes | The complain was discussed with Ahsan Jamil (HR officer) , the candidate is on waiting list said HR Officer. | Resolved. |
| 39 | 17-Mar-17 | Sorab Khan 55202-146312-5 | Kohlu 0331-8031145 | The complainant visited BEP head office and recorded his complain to Mr.Naseebullah (M&E Manager), the complainant was regarding school selection in Kohlu district, the school application form was submitted on 25th Feb-2016 and applicant name was Jamal Khan (village : Kili Darwaish abad Tamboo) but his application was not shortlisted and the BEP team selected a nearby town while both the application was submitted on same date. | 17-Mar-17 | Yes | The case was dealt by Naseebullah (M&E Manager) and Latif Marri (E.O) , they explained to him that the other application was selected for there are more enrollement of students than that of his recommended town, google map was shown to him and the BEP team made him convinced that the students of his town can also go to the selected school easily. | Resolved. |
| 40 | 20th-March-2017 | Saleh Muhammad District Member Nakas 2 | Hernai | The Complainant had an objection on the placement of Schools in the incorrect UC, i.e. Killi Paliaz pedri and killi raza muhammad. He claimed that these Schools belong to unoin council Nakas 2 but in NTS Test these are shown in Nakas 1. one post which belonged to Murgha Tangi Sar , it belongs to Union Council Nakas 2 but it is shown in Shhahrag. | 18-04-2017 | Yes | UC Corrected, Merit got final | Resolved. |

| | | | | | | | | |
|----|-----------------|---|-------------------|---|------------|-----|-------------------------------|-----------|
| 41 | 20th-March-2017 | Muhammad Ramzan S/o Amir Muhammad | Hernai, UC Nakas2 | The Complainant had an objection on the placement of Schools in the incorrect UC, i.e. Killi Paliyaz pedri and killi raza muhammad. He claimed that these Schools belong to union council Nakas 2 but in NTS Test these are shown in Nakas 1. one post which belonged to Murgha Tangi Sar , it belongs to Union Council Nakas 2 but it is shown in Shahrag. Further more two candidates Miss Nahida Tareen and Miss Sumayya Tareen are of other UC but these candidate names have been included in Nakas 2 U.C. | 18-04-2017 | Yes | UC Corrected, Merit got final | Resolved. |
| 42 | 20th-March-2017 | Esmatullah S/o Nasrullah | Hernai, UC Nakas2 | The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliyaz Pedri are located in Nakas2. | 18-04-2017 | Yes | UC Corrected, Merit got final | Resolved. |
| 43 | 20th-March-2017 | Muhammad Salim S/o Haji Muhammad Siddique | Hernai, UC Nakas2 | The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliyaz Pedri are located in Nakas2. | 18-04-2017 | Yes | UC Corrected, Merit got final | Resolved. |

| | | | | | | | | |
|----|-----------------|---|--|---|--|-----|---|-----------|
| 44 | 20th-March-2018 | Khair Shah S/o Syed Nadir Shah | Hernai, UC Nakas2 | The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliash Pedri are located in Nakas2. | 18-04-2017 | Yes | UC Corrected, Merit got final | Resolved. |
| 45 | 27-Mar-17 | Sultana D/o Rakhsh Shah | Qalat | Guidance required teacher recruitment under BEP, Community members Khadi Bangalzai has submitted Complain against Bibi Samina D/o Jalal Khan. She has changed her local certificate from Municipal Corporation to Union Council of Kalat. | District Recruitment Committee will take decision. | Yes | action taken against complain and she has recommended against vacant post, approval has also been taken by secretary education. | - |
| 46 | 3rd-Apr-17 | Naeem Shah S/o Haji Abdul Kareem 54400-0509307-3 | Ziyarat Sanjavi 0345-8326567 | In his application it was stated that his candidates who actually belong to U.C "Poi" but in NTS result which was held on 24th Jan-2017 the candidates are included in UC "Kach", He wants their names to be listed for U.C "Poi" where they really belong from. | Case is forwarded to DRC . | Yes | Case was addressed to DRC by Education Officer Babar Jaffar. And DRC listed their names for U.C Poi. | - |
| 47 | 18th April-2017 | Duniya Khan S/O Shiney Gul 56201-1770383-9 | Muhammad Rafique, Alghouri Boot House, Wasey Market Killa Saifullah | it is stated in the received document that the village kili Touda Ghazgai Ghorezai killa saifullah is selected for establishing a school as per the need of the area. As the natives are ready to facilitate Balochistan Education Project by providing Female candidates and any kind of support so it is requested to the Project Director to please do not cancel the school for the | 16-05-17 | Yes | Announced NTS for 3 times, but teacher didn't found in the UC. Other UC /tehsil Teacher can't perform their duties as the area is flung from city. As per discussion with Manger Education, the site is temporarily dropped. Will go for male option, if having less than target schools in district. | Resolved. |

| | | | | | | | | |
|----|-----------------|---|--|--|---------------|-----|---|--|
| | | | | sake of the Education and future of the local kids. | | | | |
| 48 | 12th April-2017 | abdul Qadir S/O Allah Dinah 53302-2090922-9 | Abdul Qadir S/O Allah Dinah, Nafoorullah Dinah, Majeedana Magsi, Tehsil and District Jhal Magsi. | The Complainant says that I have donated land for the establishment of Schools to Government of Balochistan Secondary Education Department after the selection of site and as promised by the representatives of BEP one post was to be nominated from my family in return to the land and rooms I gave to government but BEP did not recruit my candidate after NTS Test. | 12th Apl-2017 | Yes | – | District Recruitment Committee rejected the complaint because it is not in recruitment policy and no hiring has taken place yet in said village. |
| 49 | 19th-04-2017 | did not provide his personal information due to Tribal Affairs at their village. Only phone No. is provided i.e. 03337935647, UC LOTI, District Dera Bugti. | 3337935647 | There were three applicants who had submitted the grievance that instead of their deserving sites namely; 1. Killi Dr Saifuddin Shambani, 2. Killi Noor Muhammad Shambani, and 3. Killi Pehelwan Shambani another three sites were selected for schools i.e. 1. Killi kehlani UC Loti, 2. Goor Shamool UC Loti, and 3. Phogani UC Loti. They have appealed for Justice to Worthy Project Director. | 25-Apl-2017 | Yes | – | The applicant was contacted to provide justification to the decision taken by PMU regarding school selection criteria however the applicant did not respond. It must be noted that the District wise target of Dera Bugti was 23 and the sites were finalized on the basis of Enrolment, Distance from next level and security where construction could be executed. The said Union Council is one of the disturbed areas where project activities may not be possible to conduct. |

| | | | | | | | | |
|----|--------------|--|---|--|------------------------|-----|-------------------------|--|
| 50 | 17th-04-2017 | Sania Jalal D/o Mir Jalal Khan 51202-1521900-6 | U.C Pandran, Tehsil Kalat, Kalat. | Complain was received via TCS.She is on 2nd No. in UC and affarid of being Rejected as candidate on third no. in Uion Council Miss Bibi Sultana has submitted complian against her for changing her UC from MC Kalat to Pandran. | Case is already in DRC | Yes | case is rejected by DRC | The local cerficate was made after due date of advertizment. |
|----|--------------|--|---|--|------------------------|-----|-------------------------|--|

Court Cases (Mohtasib, Honourable High Court and Honourable Supreme Court)

| Sr # | Date | Name of the Complainant | Address With Phone Number | Gist of the Complaint | Time fixed for disposal | Whether Complaint redressed or not (Y/N) | If yes the gist of redressed | If rejected Give Reason |
|------|------------|---|------------------------------------|--|---|--|---|-------------------------|
| 1 | 08-Nov-16 | Mashoor Bibi | Jaffarabad | Complain was submitted regarding teacher recruitment.(Case against PGEB recruitment process) | Hearings to be fixed by the Hon'ble Supreme Court of Pakistan | Case Subjudised before the Hon'ble Supreme Court of Pakistan | Case pertains to PGEB project and review application is under trial in Honouable Supreme Court of Pakistan. Mr. Haroon DS (Judicial) Education Department has attended court on behalf of Education Department and projecct in Islamabad on 17-11-2016. | Pending |
| 2 | 8th Dec-16 | Zahidullah Khan s/o Zarif Khan VS SHO Police Station Hub and others | Lasbella Gulshan Colony Tehsil Hub | A Complaint was recorded before the Hon'ble High Court of Balochistan that the land gifted and dedicated for school which was supposed to be built by PGEB has been confiscated. Therefore, the Hon'ble Court through Order Dated 8.12.2016 in a case called Zahidullah Khan VS SHO Hub and others (Criminal Miscellaneous Quashment No 111 of 2013), deputed the Legal officer of GPE to visit the site and take over the possession of the said land with the help of SHO, | 16-22nd Dec,16 | yes | The land has been officially transferred in the name of "Secondary Education Department, Government of Balochistan". The details of the area of the land as well as the exact location of the land has been recorded on the mutation (Fard) document. The Revenue Record in the office of Tehseel, at Tehsil Hub, District Lasbella has been updated to this effect and the mutation document has been acquired. A new priamry school is being proposed under BEP project | Case Resolved |

| | | | | | | | | |
|---|---------------|-----------------------------|----------------|---|---|------------------|--|----------|
| | | | | Police Station Hub, and the Revenue staff. | | | | |
| 3 | 20-Dec-16 | MS. Shahina /Do Noor ur Haq | Qila Saifullah | Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment. The complainant asserted in her application that despite obtaining second position in entry test, she still was not considered for the job by PGEB authorities. | The case has been argued before the Hon'ble Ombudsman (Mohtasib) Secretariate Balochistan, Quetta, and is awaiting for the Judgment to be announced by the Hon'ble Secretariate | Judgment Pending | Mr. Jahanzaib Nasir legal Officer argued the case before the Hon'ble Ombudsman, Balochistan, and the written Judgment is awaited | Pending |
| 4 | 22nd Feb-2017 | Wadera Nihal Khan | Dera Bogti | Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding school site selection. | - | Yes | the complainant was referred to the head office of the GPE-BEP, wherein, he was satisfied and decided to withdraw the Complaint | Withdraw |

| | | | | | | | | |
|---|---------------|-----------------------------------|-----------------|--|---------------|------------------|--|-----------|
| 5 | 22nd Feb-2017 | Bashiran Bibi | Jaffarabad | Petition submitted before Honorable Supreme Court of Pakistan, regarding teacher recruitment,. | Pending | Yes | The Petition is still pending Adjudication before the Hon'ble Supreme Court of Pakistan. | Pending |
| 6 | 20-Mar-17 | Akhtar Shah Mandokhail | Zhob | complaint submitted before the Hon'ble Ombudsman, Balochistan, Quetta. The Complain complaint pertains to be against the recruitment of the Teaching staff. The copy of the complaint and the Notice from the Hon'ble Ombudsman Secretariate has been received recently (19th July-2017)and the Legal Officer has appeared before the Authority and waved off the notice. the reply to the complaint along with the relevant supporting documents will be submitted in due course. | NA | Judgment Pending | Pending | - |
| 7 | 28th Mar-2017 | Haji Muhammad Azeem Khan and Sons | Qilla Saifullah | Legal Notice from "Mr Iqbal Ahmad Kasi Advocate Law Firm", on behalf of Haji Mohammad Azeem Khan and Sons was received in dispute over Procurement for different packages including construction /Rehabilitation of schools (12 Primary and 1 Middle) in Balochistan. | 10th Apl-2017 | Yes | The Legal Notice has been replied in writing, and sent the reply through TCS Courier on Dated 10th April 2017 and the matter had then been settled and resolved. | Resolved. |

| | | | | | | | | |
|----|---------------|------------------------------|-------------------|---|---------|------------------|---|---------------|
| 8 | 5th Apl-2017 | Sahib Zadi D/o Mir Khan | Barkhan | Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding appointment as EST. | Pending | Yes | A written reply from the GPE-BEP has been submitted on 09th April 2018, and the disposal of the matter is still pending | Pending |
| 9 | 23rd Apl-2017 | Sehrish David D/o Jhon David | Nawa Killi Quetta | Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding JET teacher against Daughter Quota... | - | Yes | the complaint, after being properly written replied by GPE-BEP, has been disposed off by the Hon'ble Ombudsman on the terms that the Applicant has to approach the proper forum | Disposed off. |
| 10 | 21-Jun-17 | Bibi Rehana | Ziyarat | Constitutional Petition No 653 of 2017 has been submitted before the Hon'ble High Court of Balochistan, Quetta, on 21st June 2017 by the two Petitioners namely Bibi Rehana and Bibi Rakia against the GPE-BEP along with the Education Department, Government of Balochistan, the Deputy Commissioner and the District Education Officer of the Ziarat District, whereas, the Notice from the Hon,ble Court has been received recently on 17 july 2017. The matter pertains to be against the recruitmnt of the female | NA | Judgment Pending | Pending | - |

| | | | | | | | | |
|----|-----------|------------------------|-----------|---|---------|------------------|---------|---|
| | | | | teacher in the area. the Legal officer has appeared before the Hon'ble Court and wave off the notice. | | | | |
| 11 | 08-Jul-17 | Nasrullah S/o Allahdad | Musakhail | Constitutional Petition No 687/2017 of 2017 has been submitted before the Hon'ble High Court of Balochistan, Quetta, on 8th July 2017 by the Petitioner namely Nasrullah S/o Allahdad against the GPE-BEP along with the Education Department, Government of Balochistan, the Deputy Commissioner Musakhail District at Loralai, whereas, the Notice from the Hon,ble Court has been received recently on 08th July 2017. The matter pertains to be against the recruitmrnt of the female teacher in the area. the Legal officer has appeared before the Hon'ble Court and wave off the notice. | Pending | Judgment Pending | Pending | - |

| | | | | | | | | |
|----|---------------|-------------------------------|--|---|--------------|------------------|---|---------------|
| 12 | 17-Aug-17 | Tahira Bibi D/o Allah Dina | Jhal Magsi | the applicant seeks the transfer of her name from Union Council Jhal Magsi to Union Council Nigore, District Jhal Magsi, on the basis that according to the results of the test she secured 4th position in the latter, whereas, she has secured 12th position in U/C Jhal Magsi. | 1st Nov-2017 | Yes | The matter has been disposed of, as withdrawn | Disposed off. |
| 13 | 21st Aug-2017 | Samad Khan Saqi S/o Ab.Hameed | Samad Khan Saqi and Brothers Zhob Ph:03112121812 Mob:03208860393 | the applicant, before the Hon'ble Ombudsman, Quetta, has challenged the Bid procedure conducted by GPE-BEP, Dated 19th June 2017 at 11:00 am for Construction/Rehabilitation of School (Primary, 15 Middle) District Sherani of Package/Activity No 50 | Pending | Judgment Pending | Pending | |
| 14 | 21st Aug-2017 | Ab.Qayyum S/o Haji Habibullah | Afghan construction company Zhob Mob:03412882884 | the applicant, before the Hon'ble Ombudsman, Quetta, has challenged the Bid procedure conducted by GPE-BEP, Dated 19th June 2017 at 11:00 am for Construction/Rehabilitation of School (Primary, 12 Middle) District Zhob, Qamardin of Package/Activity No 48 | Pending | Judgment Pending | Pending | |

| | | | | | | | | |
|----|---------------|------------------------------|-------------|---|---------------|-----|--|---------|
| 15 | 26th Sep-2017 | Hajira D/o Karim Baksh | Kech | Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment. The complainant asserted in her application that despite obtaining 1st position in entry test, she still was not considered for the job by DRC. | Pending | Yes | Fresh Petition and the reply is still awaiting, still pending before the Hon'ble Ombudsman | Pending |
| 16 | 09th Oct-2017 | Saima D/o Nasir | Khuzdar | Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) regional office Khuzdar Balochistan, there was filed a complain with the averment that the recruitment committee of DRC Sikanda abad Tehsil Sorab objection on merit list and pointed out that non inclusion of name in merit list and appointed another candidate who belongs to another district. | Pending | Yes | the complaint has been received on 09th October 2017 and since then has not been pressed any further | Pending |
| 17 | 13-Oct-17 | Saadiqa Bibi D/o Niamatullah | Muslim Bagh | A Complaint was recorded before the Hon'ble High Court of Balochistan regarding teacher recruitment that the candidate is the resident of the village (Zharhi Muslim Bagh) and has passed NTS test despite that candidates from other far situated villages are hired for the posts advertised. | 30th May-2018 | Yes | The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 30th May 2018 | Pending |

| | | | | | | | | |
|----|---------------|--|--------------------------------|---|---------------|-----|--|----------------|
| 18 | 26th Oct-2017 | Zar Khatoon | — | Notice has been received from Hon'ble High Court of Balochistan from Zar Khatoon, gist of grievance is not mentioned as yet, hearing is on 21st Aug-2018. | 21st Aug-2018 | Yes | The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 21st August 2018 | Pending |
| 19 | 26th Oct-2017 | Bibi Rehana D/o Shah Buzerg Rakkia D/o Abdul Sattar | Ziyarat | A Complaint was recorded before the Hon'ble High Court of Balochistan regarding teacher recruitment, the petitioners claim that the abundant building in Killi Zargai UC Spezandi Tehsil district Ziyarat which is going to be functional via BEP so new vacancies must be created for the said school. | 19th Oct-2017 | Yes | the Petition was disposed off Dated 19 October 2017, on the terms that the School will be handed back over to the GPE-BEP, who then will functionalise the school and hand over the appointment letters to the two Petitioners | Disopossed off |
| 20 | 1st Nov-2017 | Shah Gul S/o Shadi Gul | Musa Khail | Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding school site selection. | Pending | Yes | Two written replies from the GPE-BEP have been submitted on 24th August 2017 as well as 12th February 2018, and the disposal of the matter is still pending | Pending |
| 21 | 21st Nov-2017 | Kaleemullah | Sun rise solar system Company. | Legal Notice from "Niamatullah Batezai Law Firm", on behalf of Mr Kaleemullah was received in a dispute over Procurement for scheme of 10 KV solar system for schools in Balochistan. | — | Yes | The same Legal Notice has been replied in detailed and comprehensive manner in writing and posted onthrough TCS Courier on Dated 21st November 2017 | Replied |
| 22 | 26th Dec-2017 | Rabia Kakar D/o Abdul Hmeed | Loralai | Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) reginal office Loralai | Pending | Yes | Two written replies Dated 09th January 2018 submitted in person as well as reply Dated 06th April 2018 despatched through Courier has been | Pending |

| | | | | | | | | |
|----|---------------|---|------------|--|---------|-----|--|---------------|
| | | | | Balochistan, regarding JVT teacher recruitment. | | | submitted and the outcome is still awaited | |
| 23 | 8th Jan-2018 | Saeeda Noor D/o Haji Noor Ahmed | Noshki | Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment. | Pending | Yes | Fresh Petition and the reply is still awaiting, still pending before the Hon'ble Ombudsman | Pending |
| 24 | 8th Jan-2018 | Samaira Naz | Panjgur | Petition submitted before Honorable High Court of Balochistan, regarding teacher recruitment,. | Pending | Yes | The Petition is still pending Adjudication before the Hon'ble High Court of Balochistan, at Turbat Bench. | Pending |
| 25 | 11th Jan-2018 | Taj Muammah Naik Muhammad Ghul Rasool Sons of Ali Jan | Sibi | the Plaint was initially filed before the Civil Judge Mach, wherein, the stay Application of the Plaintiff against the building of the school was dismissed after a written reply submitted by the GPE-BEP. Further, the Plaintiff then preferred an Appeal against the Order of the Civil Judge before the District and session judge (Sibi). | Pending | Yes | the matter is still pending. | Pending |
| 26 | 17th Jan-2018 | Ayesha D/o Dostain | Dera Bogti | Complain was submitted before the District and session judge (Sibi), regarding teacher recruitment. | - | Yes | The Petition has been disposed off on Dated 27th December 2017, in a terms that the matter has to be taken and decided by the District Redressal Committee (DRC) | Disposed off. |

| | | | | | | | | |
|----|---------------|--------------------------------|---------------------|---|---------|-----|---|-----------|
| 27 | 1st Mar-2018 | Sher Jan S/o Marjan | Zhob | Appeal was submitted before the District and session judge (Zhob) , dispute was over the school site selection. | - | Yes | the matter was resolved between the parties on the terms that the school building will built over the same site selected by the GPE-BEP, through proper site selection mechanism, and the troubling parties were restrained from interfering into the process of building the school. | Resolved. |
| 28 | 20th Mar-2018 | Asma Hussain D/o Nisar Hussain | Sariyab road Quetta | Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding appointment as J.V teacher.. | Pending | Yes | A written reply from the GPE-BEP has been submitted on 20th March 2018, and the disposal of the matter is still pending | Pending |
| 29 | 29th Mar-2018 | Jamila Usman | Panjgur | Petition submitted before Honorable High Court of Balochistan, regarding teacher recruitment,. | Pending | Yes | The Petition is still pending Adjudication before the Hon'ble High Court of Balochistan, at Turbat Bench. | Pending |
| 30 | 6th Apl-2018 | Amina Bibi D/o Bismillah | Dera Allahyar | Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) regional office Naseerabad at DM Jmaali Balochistan, regarding teacher recruitment. | Pending | Yes | Written Reply of the Complaint has been despatched through TCS Courier Dated 06th April 2018, and the outcome of the matter is awaited | Pending |

Procurement Grievances

| Sr # | Date | Name of the Complainant | Address With Phone Number | Gist of the Complaint | Time fixed for disposal | Whether Complaint redressed or not (Y/N) | If yes the gist of redressed | If rejected Give Reason |
|------|------|-------------------------|---------------------------|-----------------------|-------------------------|--|------------------------------|-------------------------|
|------|------|-------------------------|---------------------------|-----------------------|-------------------------|--|------------------------------|-------------------------|

| | | | | | | | | |
|---|-----------|---|-------------------------|--|----------|-----|---|-----------------------------|
| 1 | 04-Feb-16 | Israr Panezai (CEO) Shaor Org | Quetta 0300-9387204 | The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. Despite several attempts, the required information on firms behalf, as a result they did not meet eligibility criteria of qualification and thus they were considered as non-responsive. | 24-02-16 | Yes | As per Grievance Redressal Mechanism, the firm submitted review application to Grievance Redressal Committee at Education Department level. It was re-evaluated in the presence of committee chaired by Special Secretary Education. The firms submitted requisite documents and after re-evaluation, SHAOR was found to be responsive as per the technical requirements and further allowed to participate in the financial opening. | The grievance is addressed |
| 2 | 19-Feb-16 | Nadir Gul Barhech (CEO) BRSP | Quetta 0812-471437-9 | The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive. | 24-02-16 | Yes | As per Grievance Redressal Mechanism, the firm submitted review application to Grievance Redressal Committee at Education Department level. It was re-evaluated in the presence of committee chaired by Special Secretary Education. The firms submitted requisite documents and after re-evaluation, BRSP was found to be responsive as per the technical requirements and further allowed to participate in the financial opening. | The grievance is addressed |
| 3 | 16-Feb-16 | Ahmed Khan Kakar (AM) JV MDF and GRHO | Quetta 0333-7846660 | The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive. | 24-02-16 | Yes | The firm was re-evaluated in the presence of Chairman Mr. Zafar Bokhari (Special Secretary Education) , Ms,Noureen Iqbal (Manager Finance) and Mr.Hidayatullah (S.D.E). The firm, after thorough re-evaluation was found to be non-responsive as per the stated requirements. | The grievance is addressed. |

| | | | | | | | | |
|---|-----------|-----------------------------------|------------------------|---|----------|-----|--|-----------------------------|
| 4 | 22-Feb-16 | Ihtram Majid (CEO) BRDRS | Quetta 0333-7818478 | The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive. | 24-02-16 | Yes | The firm was re evaluated in the presence of Chairman Mr. Zafar Bokhari (Special Secretary Education) , Ms,Noureen Iqbal (Manager Finance) and Mr.Hidayatullah (S.D.E). BRDRS was found to be responsive as per the technical requirements and further involved in the financial opening. | The grievance is addressed. |
| 5 | 23-Feb-16 | Hameedullah Kakar Youth Org | Quetta 0346-8397898 | The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive. | 24-02-16 | Yes | The firm was re evaluated in the presence of Chairman Mr. Zafar Bokhari (Special Secretary Education) , Ms,Noureen Iqbal (Manager Finance) and Mr.Hidayatullah (S.D.E). The firm, after thorough re-evaluation was found to be non-responsive as per the stated requirements. | The grievance is addressed. |
