


QUARTERLY PROGRESS REPORT

GLOBAL PARTNERSHIP FOR EDUCATION-BALUCHISTAN EDUCATION PROJECT

SECONDARY EDUCATION DEPARTMENT

GOVERNMENT OF BALUCHISTAN

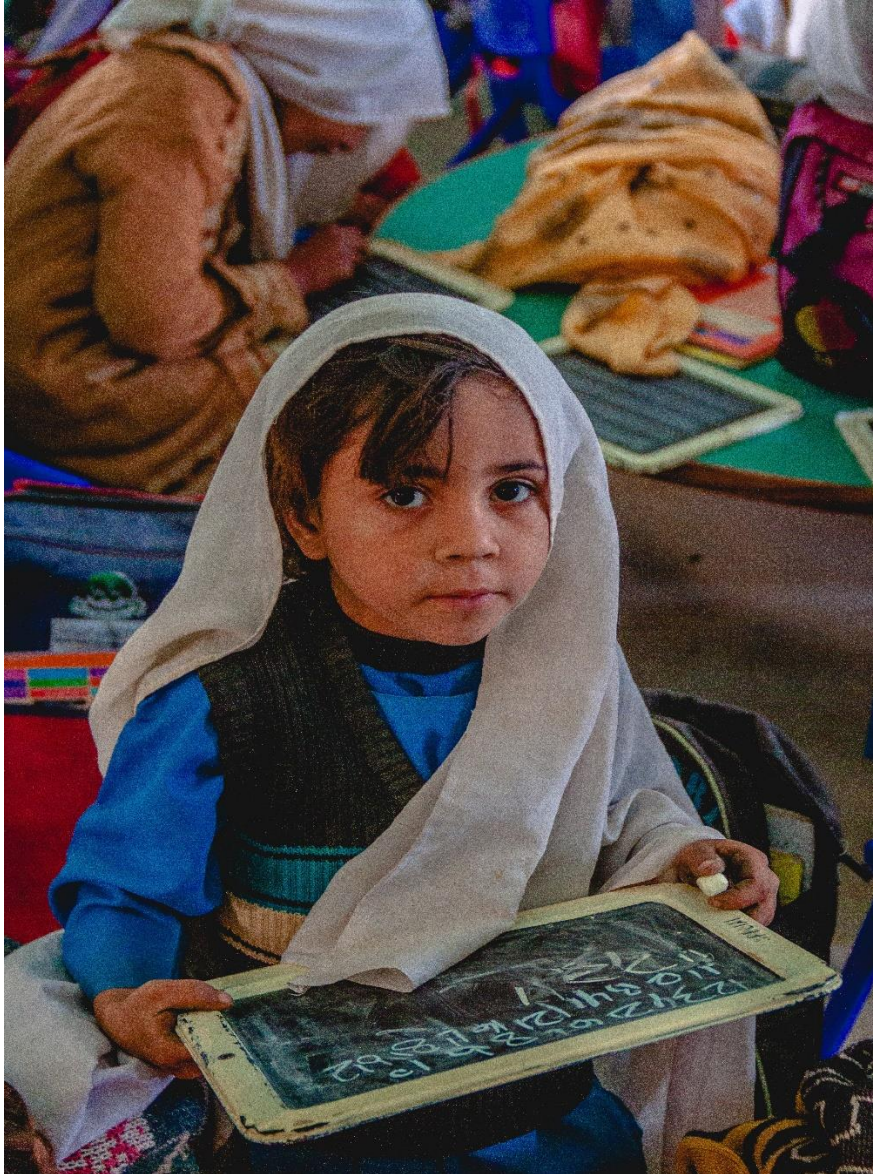

For the Quarter

Oct – Dec 2017

Project ID- P144454

Prepared by Manager M&E GPE/BEP

Executive Summary: Project Management Unit (PMU), Global Partnership for Education-Balochistan Education Project (GPE-BEP) is implementing a three year project under the supervision of World Bank. The PMU has identified and notified all 725 locations for new primary schools and all 95 primary schools to middle and 25 middle schools to high level for up-gradation with set notified criteria. 1082 teachers have been recruited and deployed for 576 newly established and upgradation schools. Recruitment of teachers for 200+ more schools is expected in coming quarter.

997 total teachers have been trained so far. However, PMU is committed to complete the training of all the target 1988 teachers by the end of upcoming second quarter .i.e. Jan-March, 2018.

In the reporting period, K-5 total 37540 students' enrollment has been reported against 389 new primary schools established, and 120 (95 Middle and 25 High) under establishment up-gradation schools. This enrolment achieves 89% of project total enrolment target where 336 more new schools enrollment is yet to be reported. It is encouraging that PMU expects 17808 more enrolment from the remaining 336 schools at average of 53 enrolment per currently established each school average. This expected enrolment will achieve project enrolment target above 100%.

Furthermore, 787 total schools have been advertised for construction works. Contracts have been awarded to start works in 709 schools. Whereas, works have been started in 570 schools.

ECE TLM material has been procured for 365 schools which will be distributed in all 845 schools and will not be procured any further, a taaleemi basta and multi-grade bags have been procured for all the 845 schools instead. In the reporting period, 165 schools have been provided with the TLM kits.

231 schools have been provided with the furniture including blackboard. ECE Program has been established in 507 schools including 389 newly established schools and 118 upgraded schools.

Contents


Results based progress	4
1. Project Development Objective	4
1.1 Girls enrolled in grades K-5 of project supported government schools	4
1.2 Boys enrolled in grades K-5 of project supported government schools.....	4
1.3. Girls enrolled in grades 6-10 of project supported government schools.....	5
2.0. Intermediate Results.....	5
2.1. Number of new primary schools established through community support	5
2.2. Number of schools upgraded from primary to middle level	6
2.3. Number of schools upgraded from middle to high/higher secondary level.....	6
2.4. Number of government schools to which furniture (incl blackboard) is provided	6
2.5. Number of schools to which TLM kits provided.....	7
2.6. Number of government schools in which ECE program established	7
2.7. Number of PTSMC members trained in targeted project schools	7
2.8. Number of teaching staff trained in the project specific schools	8
3.0. Detail table of the set target achievement against the result framework	8
4.0. Grievance Redressal Mechanism (GRM) Report Summary:.....	9
5.0. ESMP Quarterly Progress Updates	错误!未定义书签。

Results based progress

1. Project Development Objective

1.1 Girls enrolled in grades K-5 of project supported government schools

- **Progress:** The enrollment of 27802 in the bar chart is the result of the restless effort of all the PMU program sections. The enrolment/schools increased from 24257/414 of the previous quarter to 27802/507 in the reporting period at ratio from 90% to 104% of the total project enrolment target which is highly commendable. The 507 schools given in the bar include the enrolment of newly established and 120 up-gradation schools for the reporting period. The K-5 girls enrolment has been achieved over

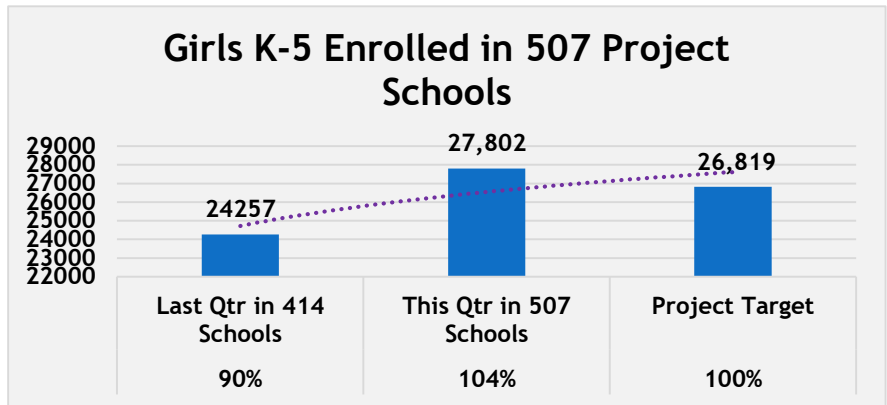


100% where 336 schools enrollment are still to be included. The remaining 336 schools at this average of 30 per school (when established) will add 10080 more enrolment which will sum the total enrolment as 37882. And this clearly projects that the achievement against this target indicator will be 142% which surpluses 42% of the girls K-5 enrolment to be highly satisfactory.

- **Lesson(s) learned:** While selecting the schools, maximum enrollment-potential locations should be selected.
- **Recommendation(s):** The Education Section should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools. The TLMs and other materials and the schools buildings should be completed ASAP to avoid the dropout.

1.2 Boys enrolled in grades K-5 of project supported government schools

- **Progress:** The enrollment of 9738 in the bar chart is the result of the restless effort of all the PMU sections. The enrolment/schools increased from 7024/414 of the previous quarter to 9738/507 in the reporting period at ratio from 45% to 63% of the total project enrolment target. The 507 schools given in the bar include the enrolment of 389 newly established and 120 up-gradation schools for the reporting period. The K-5 boys enrolment achieved so far projects that the remaining 336 schools at this average of 23 per school (when

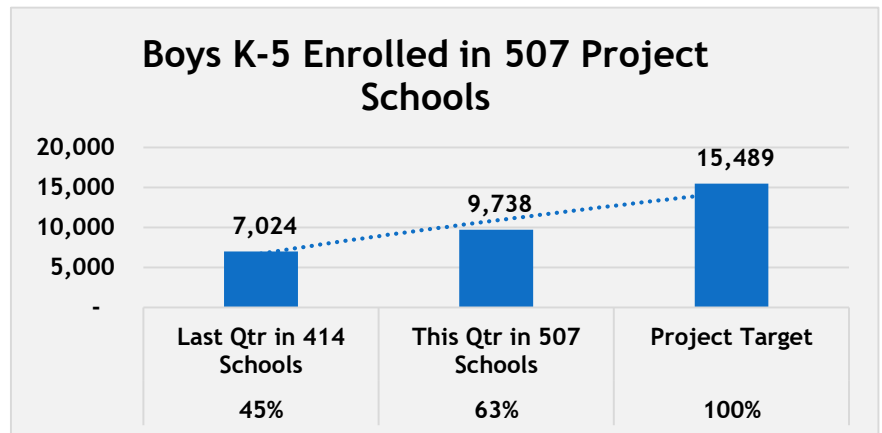


established) will add 7728 more enrolment which will sum the total enrolment as 17466. And this clearly projects that the achievement against this target indicator will be 113% which surpluses 13% of the boys K-5 enrolment to be highly satisfactory.

- **Lesson(s) learned:** While selecting the schools, maximum enrollment-potential locations should be selected.

- **Recommendation(s):** The Education Officers should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools. The TLMs and other materials and the schools buildings should be completed ASAP to avoid the dropout.

1.3. Girls enrolled in grades 6-10 of project supported government schools

- **Progress:** The enrollment of 6-10 girls in the reporting quarter is 2051 in 118 schools which is 111% of the set target. This project indicator has been achieved over 100% which is highly satisfactory. The enrollment of girls 6-10 is achieved from project supported upgradation schools. However, the construction works completion, provision of material and teachers arranged for upgraded schools is under process. The upgraded schools have entirely been selected on available higher enrolment and higher potential enrolment for the upgraded levels.

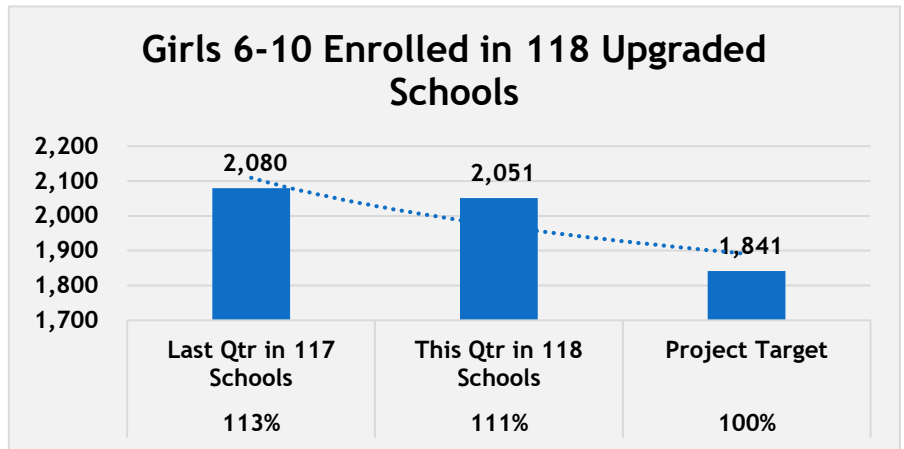


- **Lesson(s) learned:** The schools with high enrolment and feeder schools should be selected for up-gradation.
- **Recommendation(s):** The Education Officers should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools. The TLMs and other materials and the schools buildings should be completed ASAP to avoid the dropout.

2.0. Intermediate Results

2.1. Number of new primary schools established through community support


- **Progress:** The chart shows that 389 of 725 schools have been established. The chart shows that the schools establishment ratio has comparatively been well improved from last quarter as 41% and this reporting period as 54%. 1070 teachers have been hired till the reporting period for 513 primary schools which has satisfactorily improved as compared to the previous quarter number of 365 teachers for 203 schools. It is expected that all the due number of the teachers will be completed by the coming quarter.

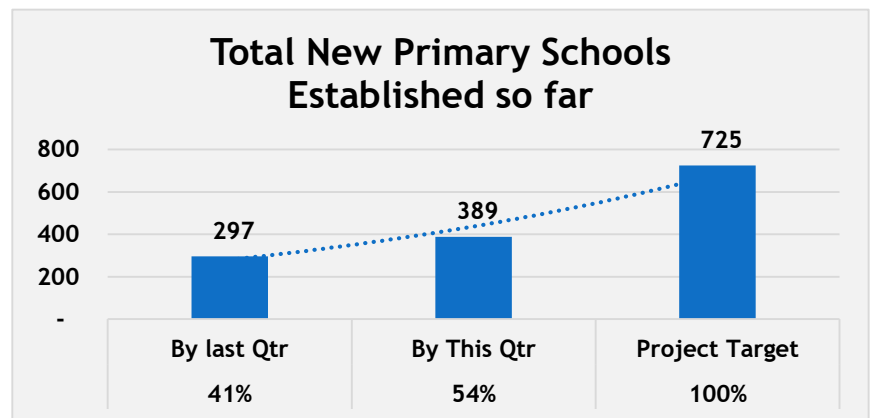

- **Lessons learned:** The PMU should ensure that all the concerned UCs villages have received the information in regard to applying for the concerned schools. Few of the concerned UCs schools did not apply for the NTS tests.
- **Recommendation(s):** Through all the available means, PMU must ensure that the concerned villages receive the information in regard to schools for applying NTS tests.


2.2. Number of schools upgraded from primary to middle level

Activity Updates: PMU has completed all the homework to proceed with the activities against this indicator. There is target of 95 middle schools upgradation from the Primary level in the project. All the 95 schools have been identified and notified. PMU has started working on upgradation activities in 99% of the upgraded schools. It is reported that 47 of 94 middle schools have started studied in class 6.

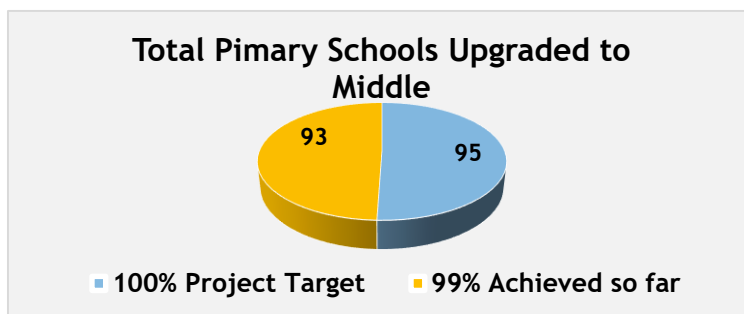


2.3. Number of schools upgraded from middle to high/higher secondary level

Activity Updates: PMU has completed all the homework to proceed with the activities against this indicator. There is target of 25 high schools upgradation from the Middle level in the project. All 25 schools have been identified and notified. PMU has started working on upgradation activities in 96% of the upgraded schools. It is reported that 8 of 24 High schools have started studied in class 9.

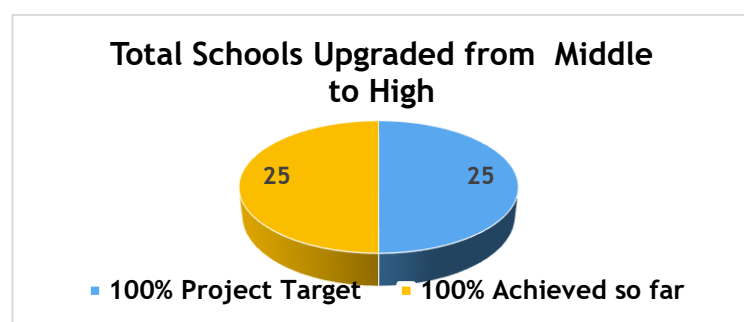

2.4. Number of government schools to which furniture (incl blackboard) is provided


Activity Updates: The procurement of all the target schools have been made. PMU has provided 231 of 845 schools with the furniture including blackboard in the reporting period. However, PMU has planned to provide 200+ schools with furniture including blackboard in the coming quarter.

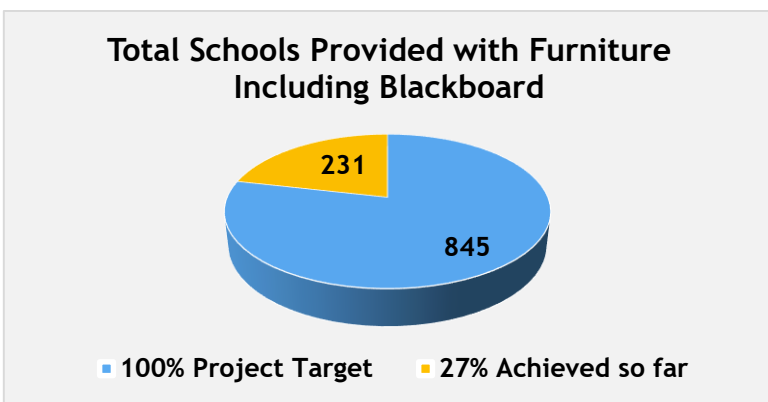

2.5. Number of schools to which TLM kits provided


Activity Updates: All ECE TLM 365 Kits have been procured which will be distributed among all 845 schools and will not be procured any further, a taaleemi basta and multi-grade bags have been procured for all the 845 schools instead.

The chart reports that PMU has provided 165 of 845 schools TLM kits so far. However, it plans to provide 300+ schools with the TLM kits in the coming quarter.

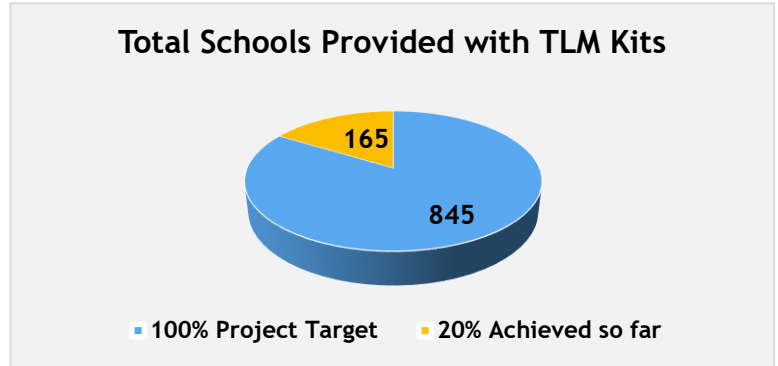


2.6. Number of government schools in which ECE program established

Activity Updates: 29 of 845 schools are established with the ECE program under the project. The number is expected increase in the coming quarter. Due to split items procurement and wide spread field, the ECE materials took time this quarter. However, the PMU has improved the supply and distribution plan and will expedite the supply and distribution in a much improved manner with increased number in the coming quarter.

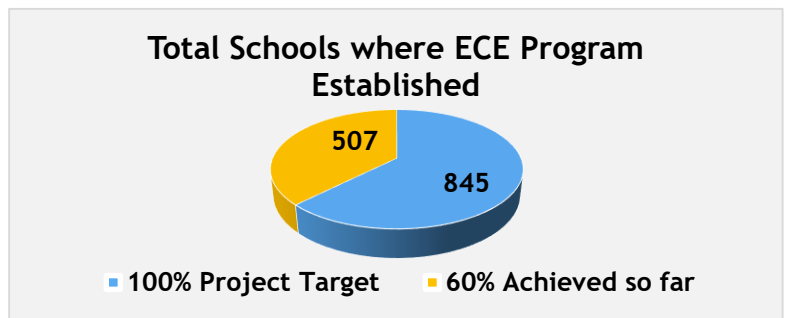

2.7. Number of PTSMC members trained in targeted project schools


Activity Updates: The number of the PTSMC members has been improved as compare to previous quarter. 1124/25% of 4465/100% PTSMC members have been trained in the reporting period. The trainings are going on. PMU expects to have much more improved number in the coming quarter.

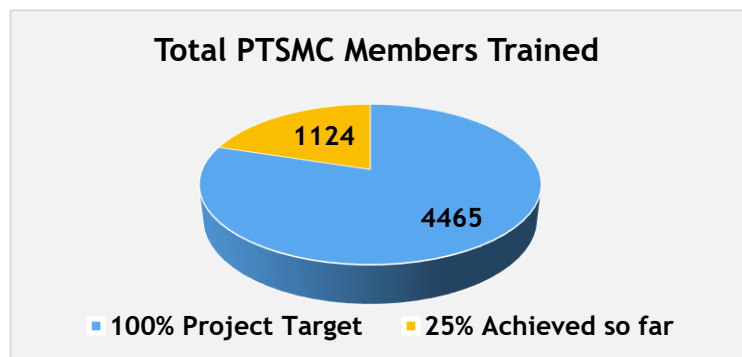

2.8. Number of teaching staff trained in the project specific schools

Activity Updates: The pie chart shows that 997 of total target teachers have been reported trained so far. This proportionates to have achieved 50% of the total project target so far.

PMU has planned more trainings in the coming quarter and will train around 300+ more teachers. The progress improves each quarter. It is shared that all 1988 teachers will be trained by the close of the second coming quarter .i.e. Jan-March, 2018.

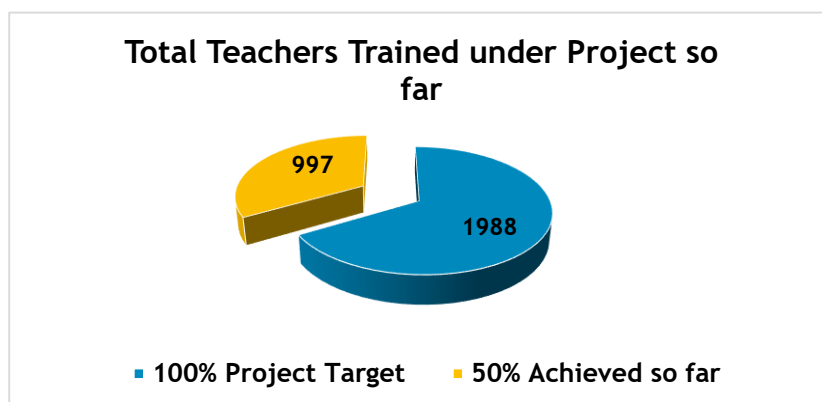

3.0. Detail table of the set target achievement against the result framework

Project Development Objectives	Target	Status	Remarks
Girls enrolled in grades K-5 of project supported government schools	26819	27802	104% Target achieved
Boys enrolled in grades K-5 of project supported government schools	15489	9738	63% Target Achieved
Student retention in project schools	75%	0	Not applicable (it will be applicable once the study session completes and the students start the next study session by the next year in Mar-Apr for winter and in Aug-Sep for summer zone.)
Girls enrolled in grades 6-10 of project supported government schools	1841	2051	111% Target Achieved
Intermediate Results			
Number of new primary schools established through community support	725	389	54% Target Achieved
Number of schools upgraded from primary to middle level	95	47	49% (the given ratio has started class 6 in the schools whereas the rest of the upgradation activities are in progress)
Number of schools upgraded from middle to high/higher secondary level	25	8	32% (the given ratio has started class 9 in the schools whereas the rest of the upgradation activities are in progress)

Number of government schools to which furniture (incl blackboard) is provided	845	231	27% Target Achieved
Number of schools to which TLM kits provided	845	165	20% Target Achieved
Number of government schools in which ECE program established	845	507	60% Target Achieved
Number of PTSMC members trained in targeted project schools	4465	1124	25% Target Achieved
Number of teaching staff trained in the project specific schools	1988	997	50% Target Achieved
Project reports generated on selected indicators			

4.0. Grievance Redressal Mechanism (GRM):

Table B (detailed sheet attached as Annex-A)

Summary of BEP-GRM Cases						
Description	Cases by Jul-Sep, 2017			Cases by Oct-Dec, 2017		
	Total Filed	Total Disposed of	Total Pending	Total Filed	Total Disposed of	Total Pending
*CRC/General Complaints	50	47	3	50	50	0
Court Cases	9	2	7	9	2	7
Procurement Cases	5	5	0	5	5	0
Total	64	54	10	64	57	7

**CRC/General Complaints include all the complaints submitted to confirm schools selection, NTS tests, and Teachers selection. Since CRC-Complaint Redress Cell is chaired by concerned division honorable Commissioner at Division level, PMU does not have any mandate to redress the cases falling under the CRC level specifically in regard to teachers selection. However, PMU GRM-PAC receives the complaints and guides the complainants to move to the CRC to file their complaint.*

5.0. ESMP Quarterly Progress Report Oct-Dec, 2017

Siting stage								
Balochistan Education Project Quarterly ESMP Implementation and Checklist Status								
S. No	District	Total Schools	Data Received during second Quarter	Data Received during third quarter	Data Received during fourth quarter	ESMP Checklist Filled Siting stage	Key Findings	Remedial Actions Taken (if any)
1	Quetta	28	21	6	1	Shin Kach Hanna	Site located near flood pathway	Trench will be made to divert flood water
2	K abdullah	39	13	25	1		No environment and social issue reported	
3	Mastung	19	8	8	3		No environment and social issue reported	
4	Pishin	29	6	18	5		No environment and social issue reported	
5	Awaran	21	1	0	20		No environment and social issue reported	
6	Khuzdar	35	23		12		No environment and social issue reported	
7	Kalat	25	9	12	4		No environment and social issue reported	
8	Lasbella	54	36	0	18	Madina Colony	Transmission line is passing over the selected site.	Relocation of transmission line.
						Jam Yousaf colony	Transmission line is passing over boundary wall of school building.	Relocation of transmission line or put casing on the transmission line.

						Pathar Colony	Site is located near flood pathway	Stone pitching wall is proposed to safe building from flood water.
9	Hernai	20	4	0	16		No environment and social issue reported	
10	K saifullah	35	14	0	21		No environment and social issue reported	
11	Sherani	20	5	0	15		No environment and social issue reported	
12	Zhob	40	12	0	28		No environment and social issue reported	
13	Ziarat	25	7	0	18		No environment and social issue reported	
14	Barkhan	31	16	0	15		No environment and social issue reported	
15	Kohlu	17	6	0	11		No environment and social issue reported	
16	Loralai	30	11	0	19		No environment and social issue reported	
17	Musakhail	27	9	0	18		No environment and social issue reported	
18	Dera Bughti	32	3	0	29		No environment and social issue reported	
19	Jaffarabad	28	16	12	0		No environment and social issue reported	

20	Jhal Magsi	20	3	7	10		No environment and social issue reported	
21	Kachi	20	9	5	6		No environment and social issue reported	
22	Naseerabad	46	27	0	19		No environment and social issue reported	
23	Sohbatpur	28	9	0	19		No environment and social issue reported	
24	Sibi	19	5	0	14		No environment and social issue reported	
				0		Elementary College	Transmission line is passing from the school building,	Relocation of transmission line or put casing on the transmission line.
25	Chaghi	30	12	0	18		No environment and social issue reported	
26	Kharan	29	4	0	25		No environment and social issue reported	
27	Noshki	25	14	0	11		No environment and social issue reported	
28	Washak	19	3	0	16		No environment and social issue reported	
29	Gwadar	25	5	20	0		No environment and social issue reported	
						Senator Ishaq	Transmission line is passing from the school building,	Relocation of transmission line or put casing on the transmission line.

30	Kech	26	3	17	6		No environment and social issue reported	
31	Punjgoor	22	1	18	3		No environment and social issue reported	

Total 401 checklists of siting stage have been received by the last quarter of the year 2017.

Construction stage checklists:

Siting stage									
Balochistan Education Project Quarterly ESMP Implementation and Checklist Status									
S. No	District	Total Schools	Data Received during First Quarter	Data Received during second Quarter	Data Received during third quarter	Data Received during fourth quarter	ESMP Checklist Filled Siting stage	Key Findings	Remedial Actions Taken (if any)
1	Quetta	28	2					No environment or social issue reported.	
2	K abdullah	39							
3	Mastung	19							
4	Pishin	29	3					No environment or social issue reported.	
5	Awaran	21							
6	Khuzdar	35							
7	Kalat	25	3					No environment or social issue reported.	
8	Lasbella	54							
9	Hernai	20							

10	K saifullah	35	7					No environment or social issue reported.	
11	Sherani	20	2					No environment or social issue reported.	
12	Zhob	40	6					No environment or social issue reported.	
13	Ziarat	25	1					No environment or social issue reported.	
14	Barkhan	31							
15	Kohlu	17							
16	Loralai	30							
17	Musakhail	27							
18	Dera Bughti	32							
19	Jaffarabad	28	4					No environment or social issue reported.	
20	Jhal Magsi	20							
21	Kachi	20							
22	Naseerabad	46	1					No environment or social issue reported.	

23	Sohbatpur	28	5					No environment or social issue reported.	
24	Sibi	19							
25	Chaghi	30							
26	Kharan	29							
27	Noshki	25	7					No environment or social issue reported.	
28	Washak	19							
29	Gwadar	25							
30	Kech	26							
31	Punjgoor	22	1					No environment or social issue reported.	

Total 42 construction stage checklists have been received during first quarter. 6 construction stage checklists have been received and reported during the second quarter of 2017.

Status of completion of remedial actions

.No	District	ESMP Checklist Filled Siting stage	Key findings	Remedial Action taken (If any)	Current status
1	Quetta	GGPS Saryab Mill near training center	Transmission lines are passing over the selected site.	Due to the community conflict construction work has not yet started. Prior starting the construction work either the relocation of transmission lines or covering the wires with the rubber pipe will be done to ensure children safety at school.	School dropped out
2	Quetta	GGPS Killi Mehrab khan Kuchlak	Transmission lines are passing near the boundary wall of a school.	Keeping in view the location of transmission lines the building is planned on the opposite site of a school building which is safe for the construction.	Not yet completed Construction work has stopped.
3	Quetta	GPS Shaheed Aymal kasi	Adjacent to solid waste dumpster	Members of PTSMCs have been contacted to remove waste from the school site.	(Contractor has been contacted and at the time of construction the waste will be removed)
	Quetta	Shin Kach Hanna	Near Flood pathway	Trench will be made to divert flood water	
4	K Abdullah	GPS Killi Agha Jan Alizai	Disputed land	Relocation of school site is under discussion.	New site has been finalized
5	K Abdullah	GPS Killi Haji Abdu Manan Toba	School site is located on top of hill	School site is under discussion	New site has been finalized
6	K Abdullah	GPS Killi Mohammad Yousaf Azadzai Dobandi	Disputed land	Relocation of school site is under discussion	School dropped out
7	Lasbella	Madina Colony	Electricity pole is in school building.	Concerned department has been contacted to relocate the pole but this process is underway and the pole has not yet been relocated. If it will not be relocated then the pole will be filled with mud till certain height to ensure child security.	Not yet completed

8	Lasbela	Madina Colony	Transmission line is passing over the selected site.	Relocation of transmission line.	
9	Lasbela	Jam Yousaf colony	Transmission line is passing over boundary wall of school building.	Relocation of transmission line or put casing on the transmission line.	
10	Lasbela	Pathar Colony	Site is located near flood pathway	Stone pitching wall is proposed to safe building from flood water.	
11	Zhob	GGPS Shahbzai	Transmission lines are passing over the selected site	Relocation of transmission line is underway with the concerned department. In case it doesn't get final then the transmission lines will be covered with the rubber pipe to ensure children safety.	Not yet completed
12	Ziarat	GGPS Kan depot.	The school site is close to highway	A traffic sign indicating school is close will be installed on the highway at the visible place.	Not yet completed
13	Ziarat	GGMIDS Pitao Zindra	The school site is close to highway	A traffic sign indicating school is close will be installed on the highway at the visible place.	Not yet completed
14	Barkhan	Rakhni City near Wapda Grid station.	The school site is close to highway	A traffic sign indicating school is close will be installed on the highway at the visible place.	Not yet completed
15	Kachi	GGPS Muhallah Muhammad Ali Meerzai Abad	Transmission lines are passing over the selected site	Relocation of transmission line is underway with the concerned department. In case it doesn't get final then the transmission lines will be covered with the rubber pipe to ensure children safety.	Not Yet completed
16	Naseerabad	GGPS Ghulam Muhammad Sarpara	The school site is close to dumpster	DFP of concerned district has been contacted to relocate the dumpster.	Not Yet completed
17	Sohbatpur	GGPS Siandad Kanrani	The school site is close to dumpster	DFP of concerned district has been contacted to relocate the dumpster.	Not Yet completed
18	Sibi	Elementary College	Transmission line is passing	Relocation of transmission line or put casing on the transmission line.	

			from the school building,		
19	Gwadar	Senator Ishaq	Transmission line is passing from the school building,	Relocation of transmission line or put casing on the transmission line.	

Annexure-A

Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason
1	3-Jan-16	Jamila Hassan	Nawa Kili Quetta 0304-3324241	Complaint application was submitted regarding NTS merit list UC Nawa kili	-	Yes	Complainant wanted to exclude ADE marks of qualified candidate. Her request was rejected by District Recruitment Committee as not valid. In recruitment policy issued by Education Department, ADE marks is applicable.	It is against Recruitment Policy notified by Education Department
2	2-May-16	Sain Dad	Sohbatpur Ghot Sain Dad kandani	Submission of letter (Subject: Cancellation of land mutation) for his candidate was not shortlisted in NTS merit list.	5/3/2016	Yes	The complainant wanted District Recruitment Committee to consider her candidate in lieu of provision of land. However, the Recruitment in the project is made through merit based recruitment policy as notified by Education Department. Therefore, complaint was rejected and recruitment is made on merit based only.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
3	2nd May-2016	Wali Dad	Qaisarabad Sohbatpur 0343-3788221	Complaint application was submitted regarding unfair recruitment of teacher, for he has devoted land for school and wants his candidate to be short-listed for his UC.	2nd May-2016	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
4	22-Jun-16	Bilqees D/o Nabi Dad	Lasbela UC Liyari	(JVT complain application was submitted) Complain application was regarding discrimination objection on NTS criteria	6/22/2016	Yes	Applicant was ineligible because she is not Intermediate pass(which is basic qualifying criteria for teachers) and also she didn't qualify NTS test.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.

5	22-Jun-16	Maryam D/o Muhammad Siddique	Lasbela UC Uthal	(JVT complain application was submitted) The community had devoted land for school on one condition iff their candidate be shortlisted.	6/22/2016	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
6	22-Jun-16	Rehana D/o Yar Muhammad	Lasbela UC Uthal	(JVT complain application was submitted) In application it is stated that the community had devoted land for school on one condition iff their candidate be shortlisted.	6/23/2016	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
7	24-Jun-16	Sumaira D/o Abdul Hakim	Lasbela UC Winder	Complain application was regarding discreditable objection on NTS criteria	6/24/2016	Yes	–	Applicant was not eligible because she is not FA and also she didn't qualified NTS test.
8	25-Jun-16	Samiya Khair D/o Khair Muhammad	Rehmdwa Noshki	(JVT complain application was submitted). Objection on merit list finalized by District Recruitment Committee.	7/7/2016	Yes	District Recruitment Committee considered her request and issue is resolved.	–
9	26-Jun-16	Saima D/o Din Muhammad	Lasbela UC Lakhara	(JVT complain application was submitted) she claims though she has done metriculation but is not shortlisted in NTS merit list.	6/26/2016	Yes	Required qualification intermediate. She is matriculate thus District Recruitment Committee rejected her complaint.	Applicant was not eligible as per approved criteria
10	27-Jun-16	Saqiba D/o Abdul Razzaq	Loralai UC Zingewal Kotazai	(JVT complain application was submitted). Complain was stated regarding rectification of UC	11/24/2016	Yes	District Recruitment Committee has verified the documents of candidates and issue was resolved	–

11	28-Jun-16	Raj Bibi D/o Muhammad Ali	Lasbela UC Uthal	(JVT complain application form was submitted) She claimed that her B.Ed and M.A degree was not considered while finalizing NTS merit list.	7/5/2016	Yes	District Recruitment Committee Lasbela considered her applicabtion and it was resolved on merit. She is on 7th number in merit	-
12	28-Jun-16	Mehbooba D/o Paida Khan 0334-2811516	Kili Saghri Loralai.	Mrs. Mehbooba compliants, that she has secured 50 marks whereas in merit list she has given only 43 marks.	11/24/2016	Yes	Issue resolved by District Recruitment Committee, on the basis of complaint merit list were checked and made correction in the numbers of the complinant.	-
13	29-Jun-16	Sakina Bibi D/o Aziz Khan	Loralai UC Zangewal	Mrs. Sakina bibi complianed that she has passed NTS test but her name is missing in merit list.	11/24/2016	Yes	Issue is resolved, as on the basis of her complaint the merit list was tallyed and and found that her name was missing due to non-availibility of her documents, but on submission/persentation of complete documents her name was included in revised merit list.	-
14	30-Jun-16	Razai Taj D/o Abdul Ghani	Loralai UC Ponga	C.T and B.A marks were not included in NTS merit result.	11/24/2016	Yes	Case was forwarded to District Recruitment Committee and requested to include her CT and BA Marks, District Recruitment Committee verified her documents and included her marks in the merit list.	-
15	4-Jul-16	Razia D/o Yar Muhammad	Lasbela UC Winder	The candidate has declared the test and is rejected for her qualification is metric and other candidate from other UC is selected.	7/15/2016	Yes	She is Matriculate only and does not meet eligibility criteria and therefore was not shortlisted and if no candidate is selected on UC level then on tehsil level candidate will be selected.	Required qualification for JVT post is intermediate with 2nd division.
16	4-Jul-16	Gul Bushra Kakar D/o Abdul Ghafor	Loralai UC Ponga	(JVT complain application was submitted) B.A and ADE marks not included	11/1/2016	Yes	Issue resolved by District Recruitment Committee , the case was forwarded to District Recruitment Committee and requested to included her BA marks, District Recruitment Committee checked her documents and included	-

							BA and ADE marks as a result she secured 2nd position and got contract.	
17	7-Jul-16	Hameeda D/o Muhammad Farooq	Lorlai UC Ponga	Complain was stated regarding rectification of UC	11/24/2016	Yes	Issue resolved by District Recruitment Committee, On the basis of her complaint, Locals of other candidates were checked and found that on candidate were not belonging to here UC and excluded all the candidates from merit list who were not belonging to the same UC.	-
18	11-Jul-16	Shahida D/o Jumma Khan	Lasbela UC Wayara	(JVT application was submitted) The community had devoted land for school on one condition iff their candidate be shortlisted and a candidate from other UC is shotlisted.	7/21/2016	Yes	Firstly she did not pass NTS test secondly if no candidate is selected on UC level then on tehsil level candidate will be selected.	District Recruitment Committee rejected the complaint because it is not in recruitment policy
19	29-Jul-16	Gulshan W/o Noorullah	Lorlai UC Thal	Higher education marks are not included in NTS merit list.	11/25/2016	Yes	Issue resolved by District Recruitment Committee , the case was forwarded to District Recruitment Committee and requested to included her BA marks, District Recruitment Committee checked her documents and included BA and ADE marks as a result she secured 2nd position and got contract.	-
20	1-Oct-16	Khan Meer	Zhob UC Wala Akram	The UC topper Ms.Farzana Zareef does not belong to UC Wala Akram but to UC Omzha(Rectification of U.C)	10/14/2016	Yes	Case resolved by District Recruitment Committee on 24-Dec-2016,	-
21	1-Nov-16	Gulshan Bibi D/o Abdul Khalique	Qila Saifullah UC Sadar Muslim bagh	It was stated in complain that her B.Ed marks were not included in merit list.	12/1/2016	Yes	Issue was addressed to District Recruitment	-

							Committee. Markes added as per documents provided	
22	1-Nov-16	Fatima Bibi D/o Hassan Khan	Qila Saifullah UC Bandad Mir zai	Complain was stated regarding rectification of UC	12/1/2016	Yes	UC Rectified by District Recruitment Committee as per documents	–
23	1-Nov-16	Zarmina Kakar	Qila Saifullah UC Sadar Muslim Bagh	Objection on ADE marks seperately.	12/1/2016	Yes	Issue was addressed by District Recruitment Committee.	–
24	3-Nov-16	Binish Kanwal	Quetta ,Kechi Baig	Complaint for JV teacher's recruitment. She claimed her name is not included in merit list.	3rd Nov-2016	Yes	Ms.Binish Kawal is included in merit list on 78th number , her total obtained marks are 57.25, her basic qualification is B.A because her F.A was scorred in 3rd div.	–
25	3-Nov-16	Fatima D/o Pehlwan	Qila Saifullah UC Sadar Muslim Bagh	Complain was stated for her B.A marks were not included in NTS merit result.	12/1/2016	Yes	Issue was addressed to District Recruitment Committee. Markes added as per documents provided	–
26	4-Nov-16	Sadiqa D/o Nadir Khan	Qila Saifullah UC Sadar Muslim Bagh	B.Ed and Physical education marks are not included in NTS merit result.	11/4/2016	Yes	Issue was adressed to District Recruitment Committee. BE.d Marks added as per dcuments provided, But physical education can't be added because they are not relavent .	–
27	4-Nov-16	Mir Alam Shahwani	Quetta 0333-7812784	Complaint was recorded regarding NTS result. Ms.Rahila Rahim had her B. Ed degree with her and is not short listed.	11/5/2016	Yes	DRC considered her request but she is on 85th nummber in merit	PTC Percentage has been given instead of B.Ed according to policy. And she is on 85th in merlit list.
28	4-Nov-16	Khair un Nisa	Qila Saifulla UC Sadar Muslimgbagh	Rectification of merit list (The Qualification marks were not included in merit list)	12/1/2016	Yes	Marks got added in meirt, Rectified by District Recruitment Committee	–
29	4-Nov-16	Sardar Bibi & Dowlat Bibi	Qila Saifulla UC Bandad Mirzai	Complain was stated regarding rectification of UC	12/1/2016	Yes	Candidate added in her UC as per her Local/residential ceritificate. Rectified by District Recruitment Committee	–

30	5-Nov-16	Gul Sumaira D/o Qalandar Khan	Zhob UC Meena Bazar	Objection on not including B.A marks in NTS merit result.	12/24/2016	Yes	Issue resolved by District Recruitment Committee . Marks added as per documents provided.	-
31	11-Nov-16	Razia Gul D/o Haji Muhammad Syed	Qila Saifullah UC Sadar Muslim Bagh	Complain was stated regarding rectification of UC	12/2/2016	Yes	Candidate added in her UC as per her Local/residential certificate. Rectified by District Recruitment Committee	-
32	11-Nov-16	Froza Khanum	UC Narezai	Complain application was regarding NTS merit list	12/24/2016	Yes	Candidate were informed about final merit as per NTS result and District Recruitment Committee working. issue resolved by District Recruitment Committee	-
33	2nd Dec- 2016	Muhammad Rafique	Musa Khail 0335-7418858	Complaint was submitted on subject of school selection. He claimed that the selected school in his town is located on 50 meters only while the school they applied for is located on 2 km distance and the enrolment of students too is more than the selected school .	27th Dec-2016	Yes	On this complaint, PMU has formed a committee of SMIP team and sent to re- visit the selected site (Killi Dargai hassankhail) and committee reported that there is no government school at the distance of 02 Km from the site. A report with GPS coordinates has been verified by SMIP team.	-
34	26th Dec- 2016	Abdul Sattar	Zhob 0313-8820907	Complaint application was submitted regarding Final Merit list of NTS test for JVT, his candidate Ms. Ameer Bakhta was 3rd in the list though she had her PTC degree with her and the candidate who was at the 2nd number had no PTC degree but that candidate had higher marks in NTS.	26th Dec-2016	Yes	His case was dealt by Naseebullah (M&E Manager), Jahanzeb Nasar(Legal Officer) and Kulsoom (Program Associate). The team listened to his complain and was explained the recruitment policy in detail , the complainant was satisfied then.	-
35	28th Dec- 2016	Abdul Aziz	Washuk 0336-3959675	Submission of letter (Subject: Cancelation of land mutation) for his candidate was not shortlisted in NTS merit list.	2nd Jan-2016	Yes	The case has been resolved the land mutated	Resolved.

36	30th Dec-2016	Khaliqdad	Muslim Bagh 0335-2700714	In advertisement the U.C for which candidate Ms.Khair un Nisa was shortlisted was Sultan Zai but actually the school is situated in Sara Gharh U.C, so Mr.Khaliqdad came to discuss the case with concern officer, for officer was not available so Naseebullah (M&E Manager) dealt.	21st Feb, 2017	Yes	Babar Jaffar (E.O) dealt the case and complainant was told that letter is sent to DC for verification of UC , as soon as UC is verified he shall be informed by BEP team. After Final merit got signed, DRC received several complaints against merit regarding UCs issue. This issue is highlighted under DRC which is being addressed. The revised final merit will be signed in coming week.	-
37	12-Mar-17	Tayyeba Rasheed 5310342662581	Kachhi Bolan	The complaint was received via e.mail . There was mentioned that the candidat Ms.Tayyeba Rasheed had applied for the post of JVT for a school in 2013 but she was not selected and there were 3 posts vacant and only one candidate was selected . As two posts are vacant so BEP should assign the vacant post to the above mentioned candidate.	13th March 2017.	Yes	The complain was discussed with Abdul Qayyum (Program Assistant) called the candidate and talked to her husband and told the complainant that this case belongs to PGEB project which is afterwards handed over to Government, so the Complainant should submit his request to Education Department but he(The candidate's husband) was rudely denying the fact and said that if your project will not facilitate us then i will go to world bank against you people.	Resolved.
38	15-Mar-17	Muhammad Naveed	Barkhan 0333-7736238	The complain was received via text on our official contact number, there was stated that the applicant Muhammad Naveed has appeared in test for (MonitoringAssociate) in RTSM PMC on 20th Nov-2016 and he also appeared in interview on 13th Dec-2016 but still has no clue about final selection.	15-Mar-17	Yes	The complain was discussed with Ahsan Jamil (HR officer) , the candidate is on waiting list said HR Officer.	Resolved.

39	17-Mar-17	Sorab Khan 55202-146312-5	Kohlu 0331-8031145	The complainant visited BEP head office and recorded his complain to Mr.Naseebullah (M&E Manager), the complainant was regarding school selection in Kohlu district, the school application form was submitted on 25th Feb-2016 and applicant name was Jamal Khan (village : Kili Darwaish abad Tamboo) but his application was not shortlisted and the BEP team selected a nearby town while both the application was submitted on same date.	17-Mar-17	Yes	The case was dealt by Naseebullah (M&E Manager) and Latif Marri (E.O) , they explained to him that the other application was selected for there are more enrolment of students than that of his recommended town, google map was shown to him and the BEP team made him convinced that the students of his town can also go to the selected school easily.	Resolved.
40	20th-March-2017	Saleh Muhammad District Member Nakas 2	Hernai	The Complainant had an objection on the placement of Schools in the incorrect UC, i.e. Killi Paliaz pedri and killi raza muhammad. He claimed that these Schools belong to union council Nakas 2 but in NTS Test these are shown in Nakas 1. one post which belonged to Murgha Tangi Sar , it belongs to Union Council Nakas 2 but it is shown in Shahrag.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
41	20th-March-2017	Muhammad Ramzan S/o Amir Muhammad	Hernai, UC Nakas2	The Complainant had an objection on the placement of Schools in the incorrect UC, i.e. Killi Paliaz pedri and killi raza muhammad. He claimed that these Schools belong to union council Nakas 2 but in NTS Test these are shown in Nakas 1. one post which belonged to Murgha Tangi Sar , it belongs to Union Council Nakas 2 but it is shown in Shahrag. Further more two candidates Miss Nahida Tareen and Miss Sumayya Tareen are of other UC but these candidate names have been included in Nakas 2 U.C.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.

42	20th-March-2017	Esmatullah S/o Nasrullah	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliaz Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
43	20th-March-2017	Muhammad Salim S/o Haji Muhammad Siddique	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliaz Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
44	20th-March-2018	Khair Shah S/o Syed Nadir Shah	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliaz Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
45	27-Mar-17	Sultana D/o Rakhsh Shah	Qalat	Guidance required teacher recruitment under BEP, Community members Khadi Bangalzai has submitted Complain against Bibi Samina D/o Jalal Khan. She has changed her local certificate from Municipal Corporation to Union Council of Kalat.	District Recruitment Committee will take decision.	Yes	Action has been taken against complaint. She has been recommended against vacant post. Approval also has been taken from Secretary Education.	Resolved

46	3rd-Apr-17	Naeem Shah S/o Haji Abdul Kareem 54400- 0509307-3	Ziyarat Sanjavi 0345-8326567	In his application it was stated that his candidates who actually belong to U.C 'Poi" but in NTS result which was held on 24th Jan-2017 the candidates are included in UC "Kach", He wants their names to be listed for U.C "Poi" where they really belong from.	Case is forwarded to DRC .	Yes	Case was intimated to DRC by Education Officer Babar Jaffer. And DRC included their name in U.C Poi list.	Resolved.
47	18th April-2017	Duniya Khan S/O Shiney Gul 56201- 1770383-9	Muhammad Rafique, Alghouri Boot House, Wasey Market Killa Saifullah	it is stated in the received document that the village killi Touda Ghazgai Ghorezai killa saifullah is selected for establishing a school as per the need of the area. As the natives are ready to facilitate Balochistan Education Project by providing Female candidates and any kind of support so it is requested to the Project Director to please do not cancel the school for the sake of the Education and future of the local kids.	5/16/2017	Yes	Announced NTS for 3 times, but teacher didn't found in the UC. Other UC /tehsil Teacher can't perform their duties as the area is flung from city. As per discussion with Manger Education, the site is temporarily dropped. Will go for male option, if having less than target schools in district.	Resolved.
48	12th April-2017	abdul Qadir S/O Allah Dinah 53302- 2090922-9	Abdul Qadir S/O Allah Dinah, Nafoorullah Dinah, Majeedana Magsi, Tehsil and District Jhal Magsi.	The Complainant says that I have donated land for the establishment of Schools to Government of Balochistan Secondary Education Department after the selection of site and as promised by the representatives of BEP one post was to be nominated from my family in return to the land and rooms I gave to government but BEP did not recruit my candidate after NTS Test.	12th Apr-2017	Yes	-	District Recruitment Committee rejected the complaint because it is not in recruitment policy and no hiring has taken place yet in said village.
49	19th-04-2017	did not provide his personal information due to Tribal Affairs at their village. Only phone No. is provided i.e. 03337935647 ,	3337935647	There were three applicants who had submitted the grievance that instead of their deserving sites namely ; 1. Killi Dr Saifuddin Shambani, 2. Killi Noor Muhammad Shambani, and 3. Killi Pehelwan Shambani another three sites were selected for schools i.e. 1. Killi	25-Apr-2017	Yes	-	The applicant was contacted to provide justification to the decision taken by PMU regarding school selection

		UC LOTI, District Dera Bugti.		kehlani UC Loti, 2. Goor Shamool UC Loti, and 3. Phogani UC Loti. They have appealed for Justice to Worthy Project Director.				criteria however the applicant did not respond. It must be noted that the District wise target of Dera Bugti was 23 and the sites were finalized on the basis of Enrolment, Distance from next level and security where construction could be executed. The said Union Council is one of the disturbed areas where project activities may not be possible to conduct.
50	17th-04-2017	Sania Jalal D/o Mir Jalal Khan 51202-1521900-6	U.C Pandran, Tehsil Kalat, Kalat.	Complain was received via TCS. She is on 2nd No. in UC and affidavit of being Rejected as candidate on third no. in Union Council Miss Bibi Sultana has submitted complian against her for changing her UC from MC Kalat to Pandran.	Case is already in DRC	Yes	The case is rejected by DRC.	The Local certificate was made after due date of the advertisement.
Court Cases (Mohtasib, Honourable High Court and Honourable Supreme Court)								
Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason

1	8-Nov-16	Mashoor Bibi	Jaffarabad	Complain was submitted regarding teacher recruitment.(Case against PGEB recruitment process)	Hearings to be fixed by the Hon'ble Supreme Court of Pakistan	Case Subjudised before the Hon'ble Supreme Court of Pakistan	Case pertains to PGEB project and review application is under trial in Honouable Supreme Court of Pakistan. Mr. Haroon DS (Judicial) Education Department has attended court on behalf of Education Department and projecct in Islamabad on 17-11-2016.	Pending
2	8th Dec-16	Zahidullah Khan s/o Zarif Khan VS SHO Police Station Hub and others	Lasbella Gulshan Colony Tehsil Hub	A Complaint was recorded before the Hon'ble High Court of Balochistan that the land gifted and dedicated for school which was supposed to be built by PGEB has been confiscated. Therefore, the Hon'ble Court through Order Dated 8.12.2016 in a case called Zahidullah Khan VS SHO Hub and others (Criminal Miscellaneous Quashment No 111 of 2013), deputed the Legal officer of GPE to visit the site and take over the possession of the said land with the help of SHO, Police Station Hub, and the Revenue staff.	16-22nd Dec,16	yes	The land has been officially transferred in the name of "Secondary Education Department, Government of Balochistan". The details of the area of the land as well as the exact location of the land has been recorded on the mutation (Fard) document. The Revenue Record in the office of Tehseel, at Tehsil Hub, District Lasbella has been updated to this effect and the mutation document has been acquired. A new priamry school is being proposed under BEP project	Case Resolved
3	20-Dec-16	MS. Shahina /Do Noor ur Haq	Qila Saifullah	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment. The complainant asserted in her application that despite obtaining second position in entry test, she still was not considered for the job by PGEB authorities.	The case has been argued before the Hon'ble Ombudsman (Mohtasib) Secretariate Balochistan, Quetta, and is awaiting for the Judgment to be announced by the Hon'ble Secretariate	Judgment Pending	Mr. Jahanzaib Nasir legal Officer argued the case before the Hon'ble Ombudsman, Balochistan, and the written Judgment is awaited	Pending

4	20-Mar-17	Akhtar Shah Mandokhail	Zhob	complaint submitted before the Hon'ble Ombudsman, Balochistan, Quetta. The Complain complaint pertains to be against the recruitment of the Teaching staff. The copy of the complaint and the Notice from the Hon'ble Ombudsman Secretariate has been received recently (19th July-2017)and the Legal Officer has appeared before the Authority and waved off the notice. the reply to the complaint along with the relevant supporting documents will be submitted in due course.	NA	Judgment Pending	Pending	–
5	21-Jun-17	Bibi Rehana	Ziyarat	Constitutional Petition No 653 of 2017 has been submitted before the Hon'ble High Court of Balochistan, Quetta, on 21st June 2017 by the two Petitioners namely Bibi Rehana and Bibi Rakia against the GPE-BEP along with the Education Department, Government of Balochistan, the Deputy Commissioner and the District Education Officer of the Ziarat District, whereas, the Notice from the Hon,ble Court has been received recently on 17 july 2017. The matter pertains to be against the recruitmnt of the female teacher in the area. the Legal officer has appeared before the Hon'ble Court and wave off the notice.	NA	Judgment Pending	Pending	–

6	8-Jul-17	Nasrullah S/o Allahdad	Musakhail	Constitutional Petition No 687/2017 of 2017 has been submitted before the Hon'ble High Court of Balochistan, Quetta, on 8th July 2017 by the Petitioner namely Nasrullah S/o Allahdad against the GPE-BEP along with the Education Department, Government of Balochistan, the Deputy Commissioner Musakhail District at Loralai, whereas, the Notice from the Hon,ble Court has been received recently on 08th July 2017. The matter pertains to be against the recruitment of the female teacher in the area. the Legal officer has appeared before the Hon'ble Court and wave off the notice.	Time fixed for hearing (29th Nov-2017)	Judgment Pending	Pending	-
7	17-Aug-17	Tahira Bibi D/o Allah Dina	Jhal Magsi	the applicant seeks the transfer of her name from Union Council Jhal Magsi to Union Council Nigore, District Jhal Magsi, on the basis that according to the results of the test she secured 4th position in the latter, whereas, she has secured 12th position in U/C Jhal Magsi.	1st Nov-2017	Yes	The matter has been disposed of, as withdrawn	Disposed off.
8	21st Aug-2017	Samad Khan Saqi S/o Ab.Hameed	Samad Khan Saqi and Brothers Zhob Ph:03112121812 Mob:03208860393	the applicant, before the Hon'ble Ombudsman, Quetta, has challenged the Bid procedure conducted by GPE-BEP, Dated 19th June 2017 at 11:00 am for Construction/Rehabilitation of School (Primary, 15 Middle) District Sherani of Package/Activity No 50	NA	Judgment Pending	Pending	

9	21st Aug-2017	Ab.Qayyum S/o Haji Habibullah	Afghan construction company Zhob Mob:03412882884	the applicant, before the Hon'ble Ombudsman, Quetta, has challenged the Bid procedure conducted by GPE-BEP, Dated 19th June 2017 at 11:00 am for Construction/Rehabilitation of School (Primary, 12 Middle) District Zhob, Qamardin of Package/Activity No 48	NA	Judgment Pending	Pending	
---	---------------	-------------------------------	---	---	----	------------------	---------	--

Procurement Grievances

Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason
1	4-Feb-16	Israr Panezai (CEO) Shaor Org	Quetta 0300-9387204	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. Despite several attempts, the required information on firms behalf, as a result they did not meet eligibility criteria of qualification and thus they were considered as non-responsive.	2/24/2016	Yes	As per Grievance Redressal Mechanism, the firm submitted review application to Grievance Redressal Committee at Education Department level. It was re-evaluated in the presence of committee chaired by Special Secretary Education. The firms submitted requisite documents and after re-evaluation, SHAOR was found to be responsive as per the technical requirements and further allowed to participate in the financial opening.	The grievance is addressed
2	19-Feb-16	Nadir Gul Barhech (CEO) BRSP	Quetta 0812-471437-9	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf,	2/24/2016	Yes	As per Grievance Redressal Mechanism, the firm submitted review application to Grievance Redressal Committee at Education Department level. It was re-evaluated in the presence of committee chaired by Special Secretary Education. The firms submitted requisite documents and after re-evaluation, BRSP was found to be responsive as per the	The grievance is addressed

				they were considered as non-responsive.			technical requirements and further allowed to participate in the financial opening.	
3	16-Feb-16	Ahmed Khan Kakar (AM) JV MDF and GRHO	Quetta 7846660 0333-	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	2/24/2016	Yes	The firm was re-evaluated in the presence of Chairman Mr. Zafar Bokhari (Special Secretary Education), Ms,Noureen Iqbal (Manager Finance) and Mr.Hidayatullah (S.D.E). The firm, after thorough re-evaluation was found to be non-responsive as per the stated requirements.	The grievance is addressed.
4	22-Feb-16	Ihtram Majid (CEO) BRDRS	Quetta 0333-7818478	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	2/24/2016	Yes	The firm was re evaluated in the presence of Chairman Mr. Zafar Bokhari (Special Secretary Education) , Ms,Noureen Iqbal (Manager Finance) and Mr.Hidayatullah (S.D.E). BRDRS was found to be responsive as per the technical requirements and further involved in the financial opening.	The grievance is addressed.

5	23-Feb-16	Hameedullah Kakar Youth Org	Quetta 0346-8397898	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	2/24/2016	Yes	The firm was re evaluated in the presence of Chairman Mr. Zafar Bokhari (Special Secretary Education) , Ms,Noureen Iqbal (Manager Finance) and Mr.Hidayatullah (S.D.E). The firm, after thorough re-evaluation was found to be non-responsive as per the stated requirements.	The grievance is addressed.
---	-----------	-----------------------------------	------------------------	---	-----------	-----	--	-----------------------------
